

**OFFSHORE OIL SCOUTS ASSOCIATION
GULF ATLANTIC**

WEEKLY DRILLING REPORT

DEEP WATER

Wednesday, April 8, 2026





OFFSHORE OIL SCOUTS

PROPRIETARY

STATEMENT



This information is provided by exclusive agreement with The Offshore Oil Scouts Association. The recipient acknowledges that the data and materials are proprietary information and trade secret, whether or not any portion thereof may be validly copyrighted or patented. Any reproduction or other use without the express written consent of The Association President will be pursued to the fullest extent of the law.

Table of Contents

NEW LOCATIONS

WALKER RIDGE Block 677 WELL PS9 CHEVRON U.S.A. INC.

MISSISSIPPI CYN Block 612 WELL DV2ST SHELL

WELLS SPUDDING

WALKER RIDGE Block 271 WELL MA4 BEACON OFFSHORE ENERGY

WALKER RIDGE Block 677 WELL PS9 CHEVRON U.S.A. INC.

ACTIVE

KEATHLEY CYN Block 247 WELL 1 BP EXPL

KEATHLEY CYN Block 918 WELL SS5ST2 ANADARKO PETROLEUM CORPOR

GREEN CYN Block 641 WELL IN3 CHEVRON U.S.A. INC.

GREEN CYN Block 743 WELL DC105 BP EXPL

GREEN CYN Block 782 WELL MD15 BP EXPLORATION & PRODUCTI

GREEN CYN Block 825 WELL 14 BP EXPL

WALKER RIDGE Block 29 WELL A12 CHEVRON U.S.A. INC.


WALKER RIDGE Block 271 WELL MA4 BEACON OFFSHORE ENERGY

WALKER RIDGE Block 425 WELL 5 MURPHY EXPLORATION & PROD

WALKER RIDGE Block 678 WELL IS2 CHEVRON U.S.A. INC.

MISSISSIPPI CYN Block 41 WELL 1 ANADARKO PETROLEUM CORPOR

MISSISSIPPI CYN Block 812 WELL KI2 SHELL

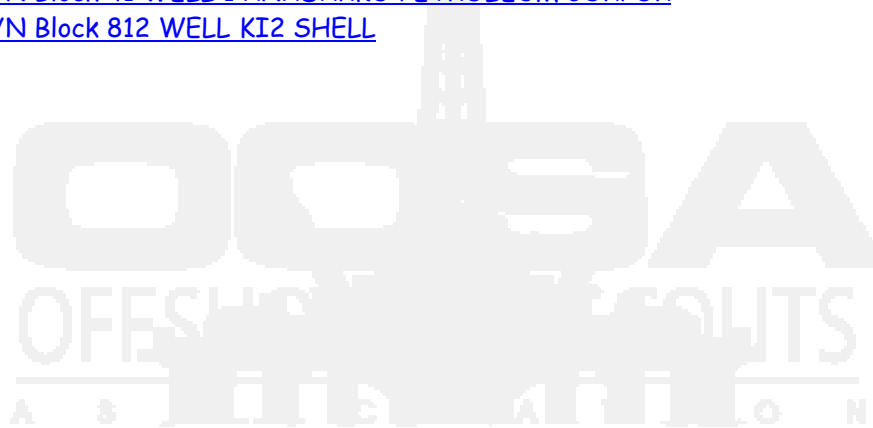

NEW LOCATIONS

WALKER RIDGE 677 PROSPECT: ST MALO
 CHEVRON U.S.A. INC. OCS: 18753 WELL: PS9 Status: NEW

678 FLD Class: DEV SS API: 60812

LOC 4924' FNL & 261' FWL of Block 00678 WALKER RIDGE
 LAT = 26.29692250 (26°17'48.921") LON = -91.09201106 (-91°05'31.240")
 X = 2,265,381 Y = 9,546,596 PMD: 30443 PTVD: 28864
 PBHL: OH 4015' FSL & 494' FEL of Block 677 WALKER RIDGE
 ATD OH: BP1: BP2: BP3: BP4: BP5:

SPUD: 04/04/2026 SUSP: COMP: RR:
 CSG= OH 36 @7452 313' ; 22 @10516

WD= 7038 KB= 101 RIG: DW CONQUEROR / TRANSOCEAN
 Date Reached TD:

04/08/2026 TD 10556 OH ST00BP00 10.5 36 @7452 W/313'P,LWD(NBGR)RAN 22 @10516,
 WOC

MISSISSIPPI CYN 612 PROSPECT: DOVER
 SHELL OCS: 33166 WELL: DV2ST Status: NEW

612 FLD Class: EXP API: 608174137401

LOC 6888' FSL & 3960' FWL of Block 00612 MISSISSIPPI CYN
 LAT = 28.38717215 (28°23'13.820") LON = -88.00093938 (-88°00'03.382")
 X = 1,318,680 Y = 10,302,888 PMD: 29401 PTVD: 28797
 PBHL: OH 4460' FSL & 4687' FWL of Block 612 MISSISSIPPI CYN
 ATD OH: BP1: BP2: BP3: BP4: BP5:

SPUD: SUSP: COMP: RR:
 CSG= OH OLD(38 @7674 ; 28 @8996 ; 22 @12508 ; 18LNR @12178-17927 ; 16LNR @17614-19775 ;
 12 1/8 @23789)

WD= 7372 KB= 102 RIG: DW PONTUS / TRANSOCEAN
 Date Reached TD:

04/08/2026 OH ST01BP00 STO #DV-2, DRILLING CEMENT TO ST

WELLS SPUDDING

WALKER RIDGE 271 PROSPECT: MONUMENT
 BEACON OFFSHORE ENERGY OCS: 35080 WELL: MA4 Status: DRLG

272 FLD Class: DEV SS API: 608124015800

LOC 344' FNL & 4428' FWL of Block 00316 WALKER RIDGE
 LAT = 26.66366648 (26°39'49.199") LON = -91.55824140 (-91°33'29.669")
 X = 2,111,148 Y = 9,677,896 PMD: PTVD:
 ATD OH: BP1: BP2: BP3: BP4: BP5:

SPUD: 04/03/2026 SUSP: COMP: RR:
 CSG= OH 42 @6725 283' ; 28 @7967

WD= 6367 KB= 75 RIG: DW ATLAS / TRANSOCEAN
 Date Reached TD:

11/12/2025 OH ST00BP00 BATCH SET
 04/08/2026 TD 8022 OH ST00BP00 11.0 42 @6725 W/283'P,LWD(ONTRANK II)28 @7967)
 WOW

WALKER RIDGE 677 PROSPECT: ST MALO
 CHEVRON U.S.A. INC. OCS: 18753 WELL: PS9 Status: NEW

678 FLD Class: DEV SS API: 60812

LOC 4924' FNL & 261' FWL of Block 00678 WALKER RIDGE
 LAT = 26.29692250 (26°17'48.921") LON = -91.09201106 (-91°05'31.240")
 X = 2,265,381 Y = 9,546,596 PMD: 30443 PTVD: 28864
 PBHL: OH 4015' FSL & 494' FEL of Block 677 WALKER RIDGE
 ATD OH: BP1: BP2: BP3: BP4: BP5:

SPUD: 04/04/2026 SUSP: COMP: RR:
 CSG= OH 36 @7452 313' ; 22 @10516

WD= 7038 KB= 101 RIG: DW CONQUEROR / TRANSOCEAN
 Date Reached TD:

04/08/2026 TD 10556 OH ST00BP00 10.5 36 @7452 W/313'P,LWD(NBGR)RAN 22 @10516,
 WOC

ACTIVE

KEATHLEY CYN **247** **PROSPECT: WEST BUMP**
BP EXPL **OCS: 25790** **WELL: 1** **Status: DRLG**

247 WC **Class: EXP** **SS** **API: 608084008000**

LOC 4687' FNL & 363' FWL **of Block** 00291 KEATHLEY CYN
LAT = 26.70216182 (26°42'07.783") **LON** = -92.63787510 (-92°38'16.350")
X = 1,758,603 **Y** = 9,689,393 **PMD**: 34548 **PTVD**: 33548
PBHL: OH 780' FSL & 757' FWL **of Block** 247 KEATHLEY CYN
ATD OH: **BP1:** **BP2:** **BP3:** **BP4:** **BP5:**

SPUD: 03/18/2026 **SUSP:** **COMP:** **RR:**
CSG= OH 36 @6100 274' ; 28 @8160 ; 22 @9979

WD= 5722 **KB=** 104 **RIG:** DW INVICTUS / TRANSOCEAN
Date Reached TD:

02/25/2026		OH	ST00BP00	LOCATION
03/18/2026		OH	ST00BP00	RIGGING UP
03/25/2026	DRLG	OH	ST00BP00 12.5	36 @6100 W/274'P,28 @8160,LWD(GR,RES,APWD)
04/01/2026	TD	OH	ST00BP00 13.0	LWD(GR,RES,APWD)22 @9979,WOC,BOP & MPD
				TESTING
04/08/2026	TD	OH	ST00BP00 13.0	REPG BOP

KEATHLEY CYN **918** **PROSPECT: HADRIAN NORTH**
ANADARKO PETROLEUM CORPO **OCS: 32654** **WELL: SS5ST2** **Status: DRLG**

875 FLD **Class: DEV** **SS** **API: 608084007902**

LOC 7073' FSL & 648' FWL **of Block** 00919 KEATHLEY CYN
LAT = 26.07798692 (26°04'40.753") **LON** = -92.05968484 (-92°03'34.865")
X = 1,948,968 **Y** = 9,463,553 **PMD**: 20461 **PTVD**: 18781
PBHL: OH 6690' FNL & 1454' FEL **of Block** 918 KEATHLEY CYN
ABHL: OH **MD:** 20434 **TVD:** 18769 N 2068' @ W 2111'
ATD OH: **BP1:** **BP2:** **BP3:** **BP4:** **BP5:**

SPUD: 03/25/2026 **SUSP:** **COMP:** **RR:**
CSG= OH OLD(36 @7774 ; 28 @8592 ; 22 @11296 ; 14 @13443 ; 9 7/8LNR @12989-19328)
7 3/4LNR @13516-20230 ; 7 3/4LNR @13354-13516

WD= 7387 **KB=** 81 **RIG:** OCEAN BLACKHAWK / NOBLE DRLG
Date Reached TD: 03/30/2026

03/25/2026		OH	ST02BP00	STO #SS-5ST,PREP TO ST
04/01/2026	TD	OH	ST02BP00 11.7	MILLED WDW @13776-13796,FIT 13.6,MPD 12.6, DRILLED FROM 13796-16616,MUD 12.5,NO MPD, LWD(GR,RES,PWD)ROLLED MUD TO 11.5,MPD 12.5, LWD(GR,RES,XBAT,DEN,NEUT,GEOTAP,PWD)PREP TO RUN 7 3/4LNR
04/08/2026	TD	OH	ST02BP00 11.8	NO MPD,RAN 7 3/4LNR @13516-20230,RAN 9 3/4 X 10 1/8 X 10 3/4 TB @13492,RAN BACK INTO HOLE & RAN A SECOND 7 3/4LNR @13354-13516, COMPTG

GREEN CYN **641** **PROSPECT: TAHITI**
CHEVRON U.S.A. INC. **OCS: 16770** **WELL: IN3** **Status: DRLG**

640 FLD **Class: INJ** **SS** **API: 608114079200**

LOC 2536' FSL & 3287' FEL **of Block** 00596 GREEN CYN
LAT = 27.35813862 (27°21'29.299") **LON** = -90.74348842 (-90°44'36.558")
X = 2,372,713 **Y** = 9,934,216 **PMD**: 28933 **PTVD**: 27185
PBHL: OH 2933' FNL & 1731' FWL **of Block** 641 GREEN CYN
ABHL: OH **MD:** 28848 **TVD:** 27104 S 5455' @ E 5006'

ACTIVE

ATD OH: 28848 BP1: BP2: BP3: BP4: BP5:

SPUD: 06/28/2025 SUSP: COMP: RR:

CSG= OH 36 @4401 308' ; 22 @6237 FIT 14.0 ; 18LNR @5785-11042 FIT 16.1 ;
16LNR @4393-19634 FIT 16.2 ; 14LNR @19233-22442 FIT 15.1 ; 9 7/8LNR @22116-28833

WD= 4012 KB= 106 RIG: DW ASGARD / TRANSOCEAN

Date Reached TD: 03/10/2026

06/18/2025		OH	ST00BP00	BATCH SET
07/02/2025	TD	6275	OH	ST00BP00 10.5 36 @4401 W/308'P, LWD (GR, PWD) 22 @6237, WOC
07/09/2025	TD	6275	OH	ST00BP00 10.5 M/OFF 7-1-25, WILL RETURN
01/21/2026	TD	6275	OH	ST00BP00 10.5 MIR TO RESUME DRILLING OPERATIONS
01/28/2026	TD	6275	OH	ST00BP00 10.5 M/ON 1-19-26, BWM, RAN RISER & BOP, PULLING BOP FOR REPAIR
02/04/2026	TD	11187	OH	ST00BP00 12.7 REPD BOP, RAN BOP, FIT 14.0 ON 22, LWD (GR, RES, PWD, NBGR) PREP TO RUN 18LNR
02/11/2026	DRLG	15067	OH	ST00BP00 13.8 MPD 14.6, RAN 18LNR @5785-11042, FIT 16.1, LWD (NBGR, EWR)
02/18/2026	TD	19780	OH	ST00BP00 14.4 MPD 15.1, LWD (EWR (NBGR, EWR) RAN 16LNR @ 4393-19634, WOC
02/25/2026	DRLG	20254	OH	ST00BP00 14.4 MPD 15.1, DRILLED OUT 16 SHOE, LOT FAILED, PUMPED LCM, CEMENT SQUEEZE, DRILL OUT, FIT 16.2 ON 16LNR, LWD (NBGR, EWR)
03/04/2026	TD	22540	OH	ST00BP00 14.4 MPD 15.1, LWD (NBGR, EWR) RAN 14LNR @ 19233-22442, PREP TO DRILL OUT & TEST LNR
03/11/2026	TD	28350	OH	ST00BP00 13.3 MPD 14.1, TOOK FIT 15.1 ON 14LNR, LWD (NBGR, EWR, DEN, NEUT, GEOTAP)
03/11/2026	TD	28350	OH	ST00BP00 13.3 MPD 14.1, TOOK FIT 15.1 ON 14LNR, LWD (NBG, REWR, DEN, NEUT, GEOTAP) DP SLIPS BROKE & PIECES WENT INTO HOLE, FSH LIKELY LOCATED AT RCD, UNSUCCESSFUL ATTEMPT TO FSH, ATTEMPTING TO RETRIEVE RCD
03/18/2026	TD	28848	OH	ST00BP00 13.9 NO MPD, RECD RCD, LWD (NBG, EWR, DEN, NEUT, GEOTAP) RAN 9 7/8LNR @22116-28833, PREP TO RUN TB
03/25/2026	TD	28848	OH	ST00BP00 13.9 NO MPD, RAN 9 7/8 X 10 3/4TB @22116, PREP TO COMP
04/01/2026	TD	28848	OH	ST00BP00 13.9 NO MPD, PREP TO COMP
04/08/2026	TD	28848	OH	ST00BP00 13.9 NO MPD, COMPTG

GREEN CYN 743 PROSPECT: ATLANTIS
BP EXPL OCS: 15607 WELL: DC105 Status: DRLG

743 FLD Class: DEV API: 608114079800

LOC 6013' FSL & 6929' FWL of Block 00743 GREEN CYN
LAT = 27.22372461 (27°13'25.409") LON = -90.03257889 (-90°01'57.284")
X = 2,604,689 Y = 9,890,173 PMD: 20782 PTVD: 18337
PBHL: OH 4104' FSL & 241' FWL of Block 743 GREEN CYN
ATD OH: BP1: BP2: BP3: BP4: BP5:

SPUD: 02/27/2026 SUSP: COMP: RR:

CSG= OH 36 @7146 230' ; 22 @10475 FIT 11.1 ; 16LNR @10311-13838 FIT 12.4 ;
13 5/8LNR @13551-17011 PIT 12.7

WD= 6838 KB= 80 RIG: OCEAN BLACK HORNET / NOBLE DRLG

Date Reached TD:

02/04/2026		OH	ST00BP00	MIR
03/04/2026	TD	10528	OH	ST00BP00 12.0 36 @7146 W/230'P, LWD (GR, RES, PWD) PREP TO RUN 22
03/11/2026	TD	10528	OH	ST00BP00 12.0 22 @10475, WOC
03/18/2026	TD	10528	OH	ST00BP00 12.0 REPG BOP
03/25/2026	TD	13840	OH	ST00BP00 10.3 MPD 11.5, FIT 11.1 ON 22, LWD (GR, RES, PWD) POOH TO RUN 16LNR
04/01/2026	TD	17180	OH	ST00BP00 11.0 MPD 11.5, RAN 16LNR @10311-13838, FIT 12.4,

ACTIVE

04/08/2026 DRLG 17239 OH ST00BP00 10.2 MPD 10.37,RAN 13 5/8LNR @13551-17011,PIT
LWD (GR, RES, PWD, SON) RNG 13 5/8LNR
12.67, LWD (GR, RES, PWD, SON)

GREEN CYN **782** **PROSPECT: MAD DOG**
BP EXPLORATION & PRODUCT **OCS: 15610** **WELL: MD15** **Status: DRLG**

826 FLD **Class: DEV** **API: 608114061200**

LOC 7228' FSL & 6166' FEL **of Block** 00782 GREEN CYN
LAT = 27.18830922 (27°11'17.913") **LON** = -90.26861424 (-90°16'07.011")
X = 2,528,234 **Y** = 9,875,548 **PMD**: 25478 **PTVD**: 22443
PBHL: OH 3471' FNL & 2401' FWL **of Block** 782 GREEN CYN
ABHL: OH **MD**: 25533 **TVD**: 22524 N 5168' @ W 7266'
ATD OH: 25533 **BP1**: **BP2**: **BP3**: **BP4**: **BP5**:

SPUD: 11/07/2013 **SUSP**: **COMP**: **RR**:
CSG= OH 36 @4886 290' ; 22 @7094 FIT 10.8 ; 16LNR @6488-12455 FIT 15.1 ;
14LNR @12154-19648 FIT 13.6

WD= 4428 **KB**= 168 **RIG**: MAD DOG SPAR / VALARIS
Date Reached TD: 02/16/2026

09/11/2013		OH	ST00BP00		(APPROVED PERMIT 9-6-13) (BATCH SET)
10/09/2013		OH	ST00BP00		M/ON 10-7-13, PREP TO RUN 36"
10/16/2013		OH	ST00BP00		M/ON 10-7-13, 36 @4886W/290' P, M/OFF 10-10-13 (WILL RET)
11/13/2013	TD	7125	OH	ST00BP00	14.0 M/ON 11-6-13, LWD (GR, RES) PREP TO RUN 22"
11/20/2013	TD	7125	OH	ST00BP00	14.0 22" @7094, WOC
11/27/2013	TD	7125	OH	ST00BP00	14.0 M/OFF 11-19-13 (WILL RETURN)
12/24/2025	TD	7125	OH	ST00BP00	14.0 M/ON 12-14-25, C/O TO DRILL AHEAD
12/31/2025	DRLG	10664	OH	ST00BP00	10.1 FIT 10.79 ON 22, LWD (GR, RES, PWD)
01/07/2026	TD	12460	OH	ST00BP00	10.2 LWD (GR, RES, PWD) PREP TO RUN 16LNR
01/14/2026	TD	12460	OH	ST00BP00	10.2 16LNR @6488-12455, PREP TO DRILL OUT & TEST LNR
01/21/2026	DRLG	18287	OH	ST00BP00	13.9 FIT 15.06 ON 16LNR, LWD (GR, RES, PWD, SON, NBGR)
01/28/2026	TD	19659	OH	ST00BP00	14.1 LWD (GR, RES, PWD, SON, NBGR) RNG 14LNR
02/04/2026	TD	19659	OH	ST00BP00	14.2 14LNR @12154-19648, WOC
02/11/2026	TD	19659	OH	ST00BP00	14.2 PREP TO DRILL OUT & TEST 14LNR
02/18/2026	TD	25533	OH	ST00BP00	13.0 FIT 13.6 ON 14LNR, LWD (GR, RES, NBGR, PWD, DEN, NEUT, SON, FPWD) CIRC BOTTOM UP
02/25/2026	TD	25533	OH	ST00BP00	13.0 WHILE BACKREAMING OUT OF HOLE, HOLE PACKED OFF & WENT TO LOSSES, STK DP @22620, PREP TO SEVER PIPE
03/04/2026	TD	25533	OH	ST00BP00	13.0 SEVERED DP, TF @21176, PREP TO PB & BYPASS
03/11/2026	TD	25533	OH	ST00BP00	13.0 REPD BOP, PREP TO BYPASS
03/18/2026	TD	25533	OH	ST00BP00	13.0 BYPASSED @19848
03/18/2026	TD	24014	BP1	ST00BP01	12.7 LWD (GR, RES, DEN, NEUT, CALP, ACOUSTIC TESTRAK) ENCOUNTERED TAR, EXPERIENCE BALLOONING & LOSSES, PULL UP TO 22810, SHUT WELL IN, C&C
03/25/2026	TD	24014	BP1	ST00BP01	12.7 PREP TO PB & BYPASS
04/01/2026	TD	24014	BP1	ST00BP01	12.7 BYPASSED @19676
04/01/2026	DRLG	23102	BP2	ST00BP02	12.7 LWD (GR, RES, PWD) ENCOUNTER TAR @23075
04/08/2026	TD	23300	BP2	ST00BP02	12.7 LWD (GR, RES, PWD) PREP TO RUN 11 7/8LNR

GREEN CYN **825** **PROSPECT: MAD DOG**
BP EXPL **OCS: 20190** **WELL: 14** **Status: DRLG**

825 FLD **Class: DEV** **API: 608114072000**

LOC 7311' FSL & 6375' FEL **of Block** 00825 GREEN CYN
LAT = 27.14594440 (27°08'45.400") **LON** = -90.31898077 (-90°19'08.331")
X = 2,512,185 **Y** = 9,859,790 **PMD**: 25223 **PTVD**: 23498
PBHL: OH 342' FSL & 5103' FEL **of Block** 825 GREEN CYN
ATD OH: **BP1**: **BP2**: **BP3**: **BP4**: **BP5**:

SPUD: 03/29/2019 **SUSP**: **COMP**: **RR**:

ACTIVE

CSG= OH 36 @5335 267' ; 22 @7645 PIT 11.8 ; 14 @17044 PIT 13.2

WD= 4986 KB= 82 RIG: WEST AURIGA / SEADRILL

Date Reached TD:

03/13/2019		OH	ST00BP00	BATCH SET
04/03/2019	TD	7692	OH	ST00BP00 10.5 36 @5335 W/267'P,LWD(ARC)22 @7645,M/OFF 4-1-19(WILL RETURN)
03/18/2026	TD	7692	OH	ST00BP00 10.5 M/ON 3-11-26,RIGGING UP
03/25/2026	TD	17080	OH	ST00BP00 10.5 MPD 11.5,PIT 11.8 ON 22,LWD(ARCVIS 900, SONVIS 900,POOH TO RUN 14
04/01/2026	DRLG	20135	OH	ST00BP00 11.7 MPD 12.2,RAN 14 @17044,PIT 13.2,LWD(GR,RES, PWD,SON)
04/08/2026	DRLG	24372	OH	ST00BP00 11.6 MPD 12.1-12.5,LWD(GR,RES,PWD,SON) DURING THE WEEK,ENCOUNTERED FORMATION LOSSES, SPOTTED LCM PILL & MPD SQUEEZE OPERATIONS, STABILIZED WELL,CONTINUED DRILLING AHEAD

WALKER RIDGE
CHEVRON U.S.A. INC.

29
OCS: 16942

PROSPECT: BIG FOOT
WELL: A12

Status: DRLG

29 FLD Class: DEV SS API: 608124005900

LOC 7578' FSL & 6940' FEL of Block 00029 WALKER RIDGE
LAT = 26.93254406(26°55'57.159") LON = -90.52019528(-90°31'12.703")
X = 2,448,260 Y = 9,780,858 PMD: 23284 PTVD: 21486
PBHL: OH 3381' FSL & 7270' FEL of Block 29 WALKER RIDGE
ABHL: OH MD: 23217 TVD: 21452 S 4194' @ W 355'
ATD OH: 23217 BP1: BP2: BP3: BP4: BP5:

SPUD: 02/24/2013 SUSP:

COMP:

RR:

CSG= OH 36 @5590 307' ; 22 @8753 FIT 12.3 ; 16LNR @5677-16836 FIT 13.0 ;
9 7/8LNR @16518-23216

WD= 5189 KB= 226 RIG: MODS 400 / NABORS OS

Date Reached TD: 02/07/2026

12/07/2011		OH	ST00BP00	'MIOCENE' (WILL BATCH SET CASING) (PERMIT APPROVED 12-1-11)
12/14/2011		OH	ST00BP00	M/ON 12-7-11,36 @5590W/307'P,M/OFF 12-8-11(WILL RET)
02/27/2013	DRLG	7085	OH	ST00BP00 16.0 M/ON 2-21-13,LWD(GR,RES,ARC,TELESCOPE,PWD)
03/06/2013	TD	8798	OH	ST00BP00 13.0 LWD(GR,RES,ARC,TELESCOPE,PWD) @8798,NO SWC, 22 @8753,M/OFF 3-2-13(WILL RET)
03/27/2013	TD	8798	OH	ST00BP00 13.0 M/ON 3-22-13,INSTALLED T/A CAP,M/OFF 3-23-13(WILL RET)
01/07/2026	TD	8798	OH	ST00BP00 13.0 M/ON 1-3-26,RIGGING UP
01/14/2026	TD	8798	OH	ST00BP00 13.0 PRESSURE TESTED CSG & TESTED BOP,DRILLING OUT CEMENT
01/21/2026	TD	16950	OH	ST00BP00 10.8 FIT 12.3 ON 22,LWD(ARCVIS,NBGR) PREP TO RUN 16LNR
01/28/2026	TD	16950	OH	ST00BP00 10.8 WHILE POOH HAD LOSSES,RAN 16LNR @ 5677-16836,PREP TO DRILL OUT & TEST LNR
02/04/2026	TD	17274	OH	ST00BP00 11.9 FIT 13.0 ON 16LNR,LWD(ARCVIS,NBGR,SONSCOPE, STETH,SADN) CUTTING LINE PLUGGED,CLEARING LINE
02/11/2026	TD	23217	OH	ST00BP00 12.3 CLEARED PLUGGED CUTTING LINE,LWD(ARCVIS, NBGR,SONSCOPE,STETH,SADN) TOOK STETH PRESSURES,RNG 9 7/8LNR
02/18/2026	TD	23217	OH	ST00BP00 12.3 9 7/8LNR @16518-23216,PREP TO SET PKR FOR PRESSURE TESTS
02/25/2026	TD	23217	OH	ST00BP00 12.3 PRESSURE TESTED LNR,RNG 9 7/8 X 11.15TB
03/04/2026	TD	23217	OH	ST00BP00 12.3 RAN 9 7/8 X 11.15TB @16518,PREP TO PULL OUTER DRILLING RISER
03/11/2026	TD	23217	OH	ST00BP00 12.3 RISER WORK
03/18/2026	TD	23217	OH	ST00BP00 12.3 RISER WORK
03/25/2026	TD	23217	OH	ST00BP00 12.3 COMPTG

ACTIVE

04/01/2026 TD 23217 OH ST00BP00 12.3 COMPTG
 04/08/2026 TD 23217 OH ST00BP00 12.3 COMPTG

WALKER RIDGE 271 **PROSPECT: MONUMENT**
BEACON OFFSHORE ENERGY OCS: 35080 **WELL: MA4** **Status: DRLG**

272 FLD **Class: DEV** SS **API: 608124015800**

LOC 344' FNL & 4428' FWL **of Block** 00316 WALKER RIDGE
LAT = 26.66366648 (26°39'49.199") **LON** = -91.55824140 (-91°33'29.669")
X = 2,111,148 **Y** = 9,677,896 **PMD:** **PTVD:**
ATD OH: **BP1:** **BP2:** **BP3:** **BP4:** **BP5:**

SPUD: 04/03/2026 **SUSP:** **COMP:** **RR:**
CSG= OH 42 @6725 283' ; 28 @7967

WD= 6367 **KB=** 75 **RIG:** DW ATLAS / TRANSOCEAN
Date Reached TD:

11/12/2025 OH ST00BP00 BATCH SET
 04/08/2026 TD 8022 OH ST00BP00 11.0 42 @6725 W/283'P,LWD(ONTRANK II)28 @7967)
 WOW

WALKER RIDGE 425 **PROSPECT: CHINOOK**
MURPHY EXPLORATION & PRO OCS: 16987 **WELL: 5** **Status: DRLG**

469 FLD **Class: DEV** **API: 608124015900**

LOC 23' FNL & 7298' FEL **of Block** 00469 WALKER RIDGE
LAT = 26.51968595 (26°31'10.869") **LON** = -90.53022803 (-90°31'48.821")
X = 2,447,902 **Y** = 9,630,697 **PMD:** 26880 **PTVD:** 26183
PBHL: OH 793' FSL & 5559' FWL **of Block** 425 WALKER RIDGE
ATD OH: **BP1:** **BP2:** **BP3:** **BP4:** **BP5:**

SPUD: 03/03/2026 **SUSP:** **COMP:** **RR:**
CSG= OH 36 @9229 309' ; 22 @12185 FIT 10.5 ; 18LNR @11917-16864 FIT 11.6

WD= 8834 **KB=** 86 **RIG:** STANLEY LAFOSSE / NOBLE DRLG
Date Reached TD:

02/18/2026 OH ST00BP00 LOCATION
 03/04/2026 OH ST00BP00 36 @9229 W/309'P,PREP TO SPUD
 03/11/2026 TD 12250 OH ST00BP00 11.5 LWD(GR,RES,PWD)RAN 22 @12185,WOC
 03/18/2026 TD 12250 OH ST00BP00 11.5 PRESSURE TESTED BOP,PREP TO DRILL OUT &
 TAKE FIT
 03/25/2026 TD 16950 OH ST00BP00 9.4 FIT 10.5 ON 22,LWD(GR,RES,PWD)RAN 18LNR @
 11917-16864,PREP TO DRILL AHEAD
 04/01/2026 DRLG 17072 OH ST00BP00 11.0 MPD 11.15,TOOK FIT 11.6 ON 18LNR,PRESSURE
 TESTED BOP,LWD(GR,RES,PWD,SON)
 04/08/2026 TD 22785 OH ST00BP00 10.5 MPD 11.1,LWD(GR,RES,PWD,SON)PREP TO RUN 16

WALKER RIDGE 678 **PROSPECT: ST MALO**
CHEVRON U.S.A. INC. OCS: 21245 **WELL: IS2** **Status: BS**

678 FLD **Class: INJ** SS **API: 608124016100**

LOC 4957' FNL & 173' FEL **of Block** 00677 WALKER RIDGE
LAT = 26.29684934 (26°17'48.658") **LON** = -91.09333694 (-91°05'36.013")
X = 2,264,947 **Y** = 9,546,563 **PMD:** **PTVD:**
ATD OH: **BP1:** **BP2:** **BP3:** **BP4:** **BP5:**

SPUD: 03/31/2026 **SUSP:** **COMP:** **RR:**
CSG= OH 36 @7451 311' ; 22 @10501

WD= 7039 **KB=** 101 **RIG:** DW CONQUEROR / TRANSOCEAN
Date Reached TD:

ACTIVE

04/01/2026 OH ST00BP00 BATCH SET,PREP TO RUN 36
 04/08/2026 TD 10550 OH ST00BP00 12.5 36 @7451 W/311'P,LWD(NBGR)RAN 22 @10501,
 M/OFF 4-4-26,WILL RETURN

MISSISSIPPI CYN **41** **PROSPECT: KING NORTH**
ANADARKO PETROLEUM CORPO **OCS: 35962** **WELL: 1** **Status: DRLG**

41 FLD **Class: DEV** **API: 608174152500**

LOC 4617' FNL & 837' FWL **of Block** 00085 MISSISSIPPI CYN
LAT = 28.92228798 (28°55'20.237") **LON** = -87.96627209 (-87°57'58.580")
X = 1,331,397 **Y** = 10,497,303 **PMD**: 17595 **PTVD**: 13804
PBHL: OH 2794' FSL & 656' FWL **of Block** 41 MISSISSIPPI CYN
ATD OH: **BP1:** **BP2:** **BP3:** **BP4:** **BP5:**

SPUD: 03/18/2026 **SUSP:** **COMP:** **RR:**
CSG= OH 36 @5571 307' ; 22 @7507 FIT 10.5 ; 18LNR @7009-9037 LOT 11.5 ;
 14 @13357 LOT 12.5

WD= 5184 **KB=** 80 **RIG:** VALARIS DS-16 / VALARIS

Date Reached TD:

03/18/2026 OH ST00BP00 RIG ON LOCATION,W/O WEATHER TO JET 36
 03/25/2026 DRLG 7680 OH ST00BP00 9.9 36 @5571 W/307'P,WHILE @7560,12.0 MUD,RAN
 22 @7507,FIT 10.5,LWD(GR,RES,APWD)
 04/01/2026 TD 9884 OH ST00BP00 10.4 MPD 11.0,WHILE @9172,LWD(GR,RES,APWD)RAN
 18LNR @7009-9037,LOT 11.5,REPG RIG
 04/08/2026 DRLG 13879 OH ST00BP00 11.3 MPD 12.0,WHILE @13389,10.4 MUD,11.0 MPD,
 LWD(GR,RES,APWD)RAN 14 @13357,LOT 12.5,
 DRILLING W/LWD(ABGR,GR,RES,X-BAT,GEOTAP,
 DEN,NEUT,APWD)

MISSISSIPPI CYN **812** **PROSPECT: KAIKIAS**
SHELL **OCS: 34461** **WELL: KI2** **Status: DRLG**

768 FLD **Class: INJ** **SS** **API: 608174152400**

LOC 6675' FSL & 5760' FEL **of Block** 00812 MISSISSIPPI CYN
LAT = 28.15827055 (28°09'29.774") **LON** = -88.96312064 (-88°57'47.234")
X = 1,008,000 **Y** = 10,223,475 **PMD**: 29835 **PTVD**: 26815
PBHL: OH 7513' FSL & 2732' FWL **of Block** 812 MISSISSIPPI CYN
ATD OH: **BP1:** **BP2:** **BP3:** **BP4:** **BP5:**

SPUD: 02/17/2026 **SUSP:** **COMP:** **RR:**
CSG= OH 38 @4832 198' ; 32 @5224 ; 28 @6311 ; 22 @8422 FIT 11.9 ;
 18LNR @7869-13124 FIT 15.3 ; 14 @24471 FIT 15.3

WD= 4547 **KB=** 87 **RIG:** STENA EVOLUTION / STENA DRILLING

Date Reached TD:

02/18/2026 OH ST00BP00 PREP TO SPUD
 02/25/2026 TD 8468 OH ST00BP00 13.0 38 @4832 W/198'P,LWD(ARCVIS)RAN 32 @5224,
 28 @6311,PREP TO RUN 22
 03/04/2026 TD 8478 OH ST00BP00 10.5 22 @8422,FIT 11.9,LWD(ARCVIS)PREP TO DRILL
 OUT
 03/11/2026 TD 13254 OH ST00BP00 11.3 LWD(ARCVIS)PREP TO RUN 18LNR
 03/18/2026 TD 24543 OH ST00BP00 14.5 18LNR @7869-13124,FIT 15.33,LWD(ARCVIS)
 PREP TO RUN 14
 03/25/2026 TD 24543 OH ST00BP00 14.5 14 @24471,DRILLING OUT CEMENT
 04/01/2026 TD 25951 OH ST00BP00 14.2 CML 14.19,FIT 15.27 ON 14,LWD(ARCVIS,STETH,
 SADN,SONVIS)RAN WL SON,TOOK MDT(FLUID SAMP)
 @24471-25825,PREP TO RUN RSWC
 04/08/2026 DRLG 28540 OH ST00BP00 14.2 CML 14.3,RECD RSWC,LWD(ARCVIS,STETH,SADN)
