

**OFFSHORE OIL SCOUTS ASSOCIATION
GULF ATLANTIC**

WEEKLY DRILLING REPORT

DEEP WATER

Wednesday, August 19, 2026





OFFSHORE OIL SCOUTS

PROPRIETARY

STATEMENT



This information is provided by exclusive agreement with The Offshore Oil Scouts Association. The recipient acknowledges that the data and materials are proprietary information and trade secret, whether or not any portion thereof may be validly copyrighted or patented. Any reproduction or other use without the express written consent of The Association President will be pursued to the fullest extent of the law.

Table of Contents

NEW LOCATIONS

ALAMINOS CYN Block 815 WELL WS504 SHELL

ACTIVE

GARDEN BANKS Block 959 WELL SP203 SHELL

ALAMINOS CYN Block 728 WELL WN103 SHELL

ALAMINOS CYN Block 857 WELL GA23 SHELL

KEATHLEY CYN Block 291 WELL 2ST BP EXPL

GREEN CYN Block 606 WELL 2 ANADARKO PETROLEUM CORPOR

GREEN CYN Block 726 WELL 6 ANADARKO PETROLEUM CORPOR

GREEN CYN Block 742 WELL DC152 BP EXPL

GREEN CYN Block 782 WELL MD15 BP EXPLORATION & PRODUCTI

GREEN CYN Block 807 WELL AP7 CHEVRON U.S.A. INC.

GREEN CYN Block 825 WELL 18 BP EXPL

WALKER RIDGE Block 107 WELL SS2 TALOS ENERGY OFFSHORE LLC

WALKER RIDGE Block 677 WELL PS9 CHEVRON U.S.A. INC.

MISSISSIPPI CYN Block 477 WELL 1 SHELL

MISSISSIPPI CYN Block 807 WELL A23ST3 SHELL

MISSISSIPPI CYN Block 816 WELL 4 LLOG EXPL


WELLS REACHING TD

KEATHLEY CYN Block 291 WELL 2ST BP EXPL

MISSISSIPPI CYN Block 816 WELL 4 LLOG EXPL

SUSPENDED

ALAMINOS CYN Block 728 WELL WN103 SHELL

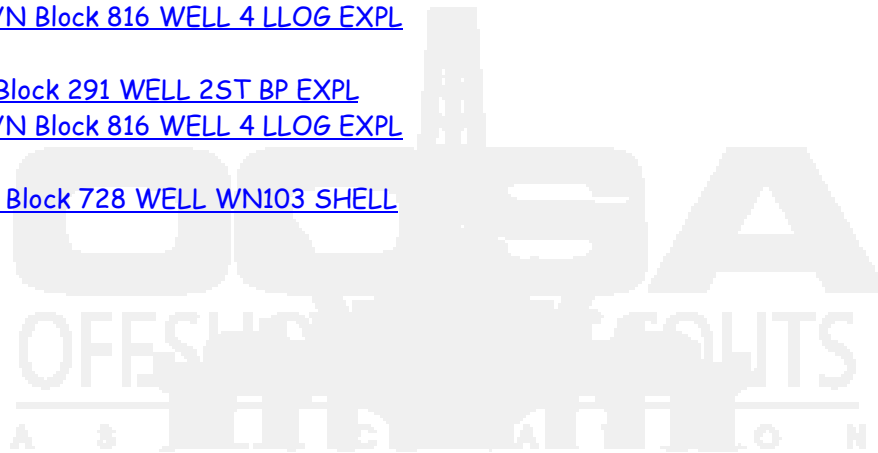

ALAMINOS CYN
SHELL

OCS: 19409

WELL: WS504

Status: NEW

API: 608054012000

WD= 9067 KB= RIG: DW POSEIDON / TRANSOCEAN
Date Reached TD:

08/19/2026	OH	ST00BP00	LOCATION
------------	----	----------	----------

ACTIVEGARDEN BANKS
SHELL959
OCS: 30876PROSPECT: SPARTA
WELL: SP203

Status: DRLG

958 FLD

Class: DEV

SS

API: 608074033200

LOC 7507' FNL & 3623' FWL of Block 00959 GARDEN BANKS
 LAT = 27.04154036 (27°02'29.545") LON = -92.23735115 (-92°14'14.464")
 X = 1,888,583 Y = 9,813,293 PMD: 31560 PTVD: 30592
 PBHL: OH 6135' FSL & 1793' FWL of Block 959 GARDEN BANKS
 PBHL: BP15694' FSL & 1665' FWL of Block 959 GARDEN BANKS
 ABHL: OH MD: 31158 TVD: 30655 S 2211' @ W 1830'
 ATD OH: BP1: BP2: BP3: BP4: BP5:

SPUD: 09/05/2025 SUSP: COMP: RR:
 CSG= OH 42 @4630 274' ; 32 @5559 ; 28 @6704 ; 22 @10164 FIT 15.4 ; 14 @24315 FIT 16.7

WD= 4269 KB= 87 RIG: STENA EVOLUTION / STENA DRILLING
 Date Reached TD:

Date	Time	OH	ST00BP00	Batch Set
06/04/2025		OH	ST00BP00	BATCH SET
09/10/2025	DRLG	6108	OH	ST00BP00 12.1 42 @4630 W/274'P, 32 @5559, M/OFF 9-6-25, M/ON 9-8-25, LWD (GR, RES, PWD)
09/17/2025	TD	10214	OH	ST00BP00 13.0 28 @6704, LWD (GR, RES, PWD) RNG 22
09/24/2025	TD	10214	OH	ST00BP00 13.0 22 @10164, M/OFF 9-15-25, WILL RETURN
12/10/2025	TD	10214	OH	ST00BP00 13.0 M/ON 12-6-25, RIGGING UP
12/17/2025	TD	10214	OH	ST00BP00 13.0 FINISHED RIGGING UP, PREP TO DRILL AHEAD
12/24/2025	TD	24365	OH	ST00BP00 16.3 CML 15.9, FIT 15.4 ON 22, LWD (GR, RES, PWD, SON) PREP TO RUN 14
12/31/2025	DRLG	24535	OH	ST00BP00 16.3 CML 16.1, RAN 14 @24315, FIT 16.66, LWD (GR, RES, PWD)
01/07/2026	DRLG	31158	OH	ST00BP00 16.3 CML 16.3, LWD (GR, RES, PWD) ORIG MD, 31108, TVD 30615
01/14/2026	TD	31158	OH	ST00BP00 16.3 CML 16.3, WELL CONTROL WORK DECISION NOT TO DRILL AHEAD, PREP TO PB & BYPASS
01/21/2026	TD	31158	OH	ST00BP00 16.3 CML 16.3, SET 2 OPEN HOLE PLUGS, PREP TO SET KICKOFF PLUG & BYPASS
01/28/2026	TD	31158	OH	ST00BP00 16.3 CML 16.3, SET KICKOFF PLUG, TOC @23915, PREP TO BYPASS
02/04/2026	TD	31158	OH	ST00BP00 16.3 CML 16.3, DRILLED CEMENT W/BYPASS BHA, OBSERVED LOSSES INDICATING INADEQUATE CEMENT, COULD NOT BYPASS, SET ADDL PLUG, TOC @ 24439, SETTING PLUG #5 TO BYPASS
02/11/2026	TD	31158	OH	ST00BP00 16.3 CML 16.3, SET PLUG #5, TOC @23924, PREP TO T/A, WILL RETURN TO BYPASS
02/18/2026	TD	31158	OH	ST00BP00 16.3 CML 16.3, T/A 2-10-26, WILL RETURN
06/24/2026	TD	31158	OH	ST00BP00 16.3 M/ON 6-21-26, PREP TO RE-ENTER & BYPASS ORIG PTDS: 31527 MD, 31019 TVD
07/01/2026	TD	31158	OH	ST00BP00 16.3 CML 16.3, RAN RISER & BOP, PREP TO PB & BYPASS
07/08/2026	TD	31158	OH	ST00BP00 16.3 CML 16.3, REPD CML SYSTEM, PREP TO RUN WHIPTSTOCK & BYPASS
07/15/2026	TD	31158	OH	ST00BP00 16.3 CML 16.3, RAN & SET WHIPTSTOCK TO MILL WDW @ 23448, WHILE MILLING WDW MILLS TWISTED OFF, TF @23404, PREP TO SET PLUG TO ISOLATE FSH THEN RUN NEW WHIPTSTOCK & BYPASS
07/22/2026	TD	31158	OH	ST00BP00 16.3 CML 16.3, SET PKR @23370, SET WHIPTSTOCK, BEGIN MILLING, POOH, OBSERVED MISSING MILLS, TF @23290, PREP TO FSH
07/29/2026	TD	31158	OH	ST00BP00 16.3 CML 16.3, RECOVERED FSH, MILLED WDW @ 23332-23365, BYPASSED @23365
07/29/2026	TD	23408	BP1	ST00BP01 15.9 CML OFF, POOH W/MILLING BHA, PREP TO RUN DRILLING BHA
08/05/2026	DRLG	26534	BP1	ST00BP01 16.2 CML 16.2, TOOK FIT ON WDW 16.53, LWD (ARCVIS)
08/12/2026	TD	31222	BP1	ST00BP01 16.2 CML 16.3, LWD (ARCVIS) OBSERVED INFLUX, WELL CONTROL OPERATIONS

ACTIVE

08/19/2026 TD 31342 BP1 ST00BP01 16.2 CML 16.4,PERFORMED WELL CONTROL OPERATIONS,
LWD(ARCVIS)PREP TO RUN 10.05LNR

ALAMINOS CYN	728	PROSPECT: WHALE	
SHELL	OCS: 31195	WELL: WN103	Status: SUSP

728 WC **Class: DEV** **API: 608054011900**

LOC 1627' FSL & 3169' FEL **of Block** 00728 ALAMINOS CYN
LAT = 26.23005494 (26°13'48.198") **LON** = -94.72843942 (-94°43'42.382")
X = 1,073,951 **Y** = 9,521,467 **PMD**: 23560 **PTVD**: 21452
PBHL: OH 7352' FSL & 4941' FEL **of Block** 728 ALAMINOS CYN
PBHL: BP17366' FSL & 4955' FEL **of Block** 728 ALAMINOS CYN
ABHL: BP1 **MD**: 23590 **TVD**: 21460 N 5783' @ W 1792'
ATD OH: 19877 **BP1**: 23590 **BP2**: **BP3**: **BP4**: **BP5**:
SPUD: 11/03/2025 **SUSP**: 08/16/2026 **COMP**: **RR**: 08/16/2026
CSG= OH 38 @8931 198' ; 28 @9843 ; 22 @14790 FIT 12.0 ;
 16.08LNR @14387-16395 FIT 12.1 ; 14LNR @16060-19547 FIT 12.6 ;
 9 5/8LNR @19245-23585

WD= 8631 **KB**= 102 **RIG**: DW POSEIDON / TRANSOCEAN
Date Reached TD: 07/06/2026

10/15/2025		OH	ST00BP00	BATCH SET
11/12/2025	DRLG	14828	OH	ST00BP00 10.0 MPD 10.62,RAN 38 @8931 W/198'P,28 @9843, LWD(GR,RES,PWD)
11/19/2025	TD	14840	OH	ST00BP00 10.5 MPD 10.73,LWD(GR,RES,PWD)22 @14790,M/OFF 11-13-25,WILL RETURN
05/20/2026	TD	14840	OH	ST00BP00 10.5 M/ON 5-14-26,RNG BOP & RISER TO RESUME DRILLING OPERATIONS
05/27/2026	TD	19877	OH	ST00BP00 10.4 MPD 10.94,TOOK FIT 12.06 ON 22,LWD(ARCVIS, SONSCOPE)PREP TO RUN 13 5/8
06/03/2026	TD	19877	OH	ST00BP00 10.4 MPD 10.94,ATTEMPTED TO RUN 13 5/8,COULD NOT GET DOWN,PREP TO C/O & RE-RUN 13 5/8
06/10/2026	TD	19877	OH	ST00BP00 10.8 MPD 10.9,C/O,ATTEMPTED TO RE-RUN 13 5/8, COULD NOT GET DOWN,POOH W/CSG STRING
06/17/2026	TD	19877	OH	ST00BP00 10.8 MPD 10.9,POOH W/13 5/8LNR,PUMPED CEMENT PLUGS @14684,PREP TO BYPASS
06/24/2026	TD	19877	OH	ST00BP00 10.8 MPD 10.9,BYPASSED @14850
06/24/2026	TD	16450	BP1	ST00BP01 10.5 MPD 10.7,TOOK FIT 12.04 ON 22,LWD(ARCVIS) RAN 16.08LNR @14387-16395,PREP TO DRILL OUT,ORIG HOLE PTD:23534 MD,21448 TVD
07/01/2026	TD	19665	BP1	ST00BP01 11.2 MPD 11.4,TOOK FIT 12.07 ON 16.08LNR, LWD(ARCVIS)RAN 14LNR @16060-19547,PREP TO DRILL OUT
07/08/2026	TD	23590	BP1	ST00BP01 9.5 MPD 10.3,TOOK FIT 12.61 ON 14,LWD(ARCVIS, SONSCOPE,STETH,SADN)C&C,TAKING FPWD PRESSURES
07/15/2026	TD	23590	BP1	ST00BP01 9.5 MPD 10.3,TOOK FPWD PRESSURES,PERFORMED OPEN HOLE LOT TO 12.12,RAN WL,HDRS,HNGS, PPC,MAST,NGI @23590,RAN 9 5/8LNR @ 19245-23585,PREP TO RUN 9 5/8 X 10 3/4TB
07/22/2026	TD	23590	BP1	ST00BP01 9.5 MPD 10.3,RAN 9 5/8 X 10 3/4TB @19255,C/O, PREP TO COMP
07/29/2026	TD	23590	BP1	ST00BP01 9.5 MPD 10.3,COMPTG
08/05/2026	TD	23590	BP1	ST00BP01 9.5 MPD 10.3,COMPTG
08/12/2026	TD	23590	BP1	ST00BP01 9.5 MPD 10.3,COMPTG
08/19/2026	TD	23590	BP1	ST00BP01 9.5 MPD 10.3,R.R.PERFORMING END OF WELL MAINTENANCE

ALAMINOS CYN	857	PROSPECT: GREAT WHITE	
SHELL	OCS: 17565	WELL: GA23	Status: TA

857 FLD **Class: DEV** **API: 608054006000**

LOC 2836' FNL & 4006' FWL **of Block** 00857 ALAMINOS CYN

ACTIVE

LAT = 26.12847000 (26°07'42.492") **LON** = -94.89819000 (-94°53'53.484")

X = 1,017,766 **Y** = 9,485,324 **PMD**: 19046 **PTVD**: 18802

PBHL: OH 3934' FNL & 2485' FWL **of Block** 857 ALAMINOS CYN

PBHL: BP13848' FNL & 2560' FWL **of Block** 857 ALAMINOS CYN

ATD OH: **BP1:** **BP2:** **BP3:** **BP4:** **BP5:**

SPUD: 11/08/2007 **SUSP**:

COMP:

RR:

CSG= OH 36 @8084 193' ; 22 @9169 ; 16 @10476 LOT 9.9 ;

13 3/8LNR @10409-11931 LOT 10.4 ; 11 3/4 @14033 LOT 10.2 ; 9 5/8LNR @13636-14622

WD= 7819 **KB**= 203 **RIG**: H&P 205 / H&P DRLG

Date Reached TD:

10/31/2007		OH		(BATCH SET)
11/14/2007 TD	10517	OH	10.0	36 @8084W/193'P,LWD (GR,RES,PWD) @9169,NO SWC,22 @9169,LWD (GR,RES,PWD) @10517,NO SWC,16 @10476,M/OFF 11-10-07 (WILL RET
01/07/2026 TD	10517	OH	ST00BP00 10.0	M/ON 1-4-26,RIGGING UP
01/14/2026 TD	11964	OH	ST00BP00 9.0	MPD 9.4,LOT 9.87 ON 16,LWD (GR,RES,PWD) PREP TO RUN 13 3/8LNR
01/21/2026 TD	11964	OH	ST00BP00 9.0	MPD 9.4,RAN 13 3/8LNR @10409-11931,PREP TO DRILL OUT
01/28/2026 TD	14083	OH	ST00BP00 9.6	MPD 10.1,LOT 10.44 ON 13 3/8LNR,LWD (GR,RES,PWD) PREP TO RUN 11 3/4
02/04/2026 TD	14096	OH	ST00BP00 8.6	MPD OFF,RAN 11 3/4 @14033,LOT 10.23,UNABLE TO OPEN REAMER,TIH W/NEW BHA
02/11/2026 TD	14096	OH	ST00BP00 8.6	MPD OFF,PERFORMED RIG MAINTENANCE,PREP TO DRILL AHEAD
02/18/2026 TD	14647	OH	ST00BP00 8.6	MPD OFF,LWD (GR,RES,PWD) PREP TO RUN 9 5/8LNR
02/25/2026 TD	14647	OH	ST00BP00 8.6	MPD,PERFORMED CHECK TRIP W/DUMB IRON BHA,WOW TO RUN 9 7/8LNR
03/04/2026 TD	14647	OH	ST00BP00 8.6	MPD OFF,PERFORMED ANOTHER CHECK TRIP W/DUMB IRON BHA,RAN 9 5/8LNR @13636-14622,PREP TO DRILL OUT 9 5/8 SHOETRACK
03/11/2026 TD	14647	OH	ST00BP00 9.4	MPD OFF,BEGAN DRILLING 9 5/8 SHOETRACK,BHA GOT STK @14642,UNABLE TO JAR FREE,PREP TO RUN WL TO DETERMINE FREE POINT
03/18/2026 TD	14647	OH	ST00BP00 9.4	MPD OFF,BACKED OFF,TF @14416,COULD NOT RECOVER FSH,PREP TO PUMP CEMENT PLUG ON TOF TO BYPASS
03/25/2026 TD	14647	OH	ST00BP00 9.4	MPD OFF,T/A 3-23-26,WILL RETURN TO BYPASS
07/01/2026 TD	14647	OH	ST00BP00 9.4	MPD OFF,M/ON 6-29-26,PREP TO PB & BYPASS ORIG PTDS: 18967 MD,18736 TVD
07/08/2026 TD	14647	OH	ST00BP00 9.4	MPD OFF,RIG MAINTENANCE,TSTD BOP,PREP TO BYPASS
07/15/2026 TD	14647	OH	ST00BP00 9.4	PREP TO CUT & PULL 11 3/4 & BYPASS IN THE OPEN HOLE
07/22/2026 TD	14647	OH	ST00BP00 9.4	C/O WELLBORE,PREP TO CUT & PULL 11 3/4 TO BYPASS
07/29/2026 TD	14647	OH	ST00BP00 9.4	MPD OFF,CUT 11 3/4 @12244,POOH W/11 3/4
08/05/2026 TD	14647	OH	ST00BP00 9.4	MPD OFF,SET CEMENT PLUG IN OPEN HOLE,TOC @ 11770,PREP TO BYPASS
08/12/2026 TD	14647	OH	ST00BP00 9.4	MPD OFF,RIG MAINTENANCE,PREP TO RIH W/DRILLING BHA TO BYPASS
08/19/2026 TD	14647	OH	ST00BP00 9.4	MPD OFF,M/OFF 8-14-26,WILL RETURN TO BYPASS,PAUSING OPERATIONS TO PERFORM ESP REPLACEMENT AT PERDIDO

KEATHLEY CYN

BP EXPL

291

OCS: 19545

PROSPECT: WEST BUMP

WELL: 2ST

Status: DRLG

291 WC

Class: EXP

SS

API: 608084008001

LOC 4687' FNL & 363' FWL **of Block** 00291 KEATHLEY CYN

LAT = 26.70216182 (26°42'07.783") **LON** = -92.63787509 (-92°38'16.350")

X = 1,758,603 **Y** = 9,689,393 **PMD**: 36146 **PTVD**: 33517

ACTIVE

PBHL: OH 3808' FNL & 5334' FWL **of Block** 291 KEATHLEY CYN

ATD OH: 31675 **BP1:** 35454 **BP2:** **BP3:** **BP4:** **BP5:**

SPUD: 07/01/2026 **SUSP:**

COMP:

RR:

CSG= OH OLD(36 @6100 ; 28 @8160 ; 22 @9979 ; 18LNR @9753-14850 ; 16LNR @5847-20978 ; 14 @27696 ; 11 7/8LNR @21122-29801)

11 7/8LNR @26621-30105 FIT 16.0

WD= 5722 **KB=** 104 **RIG:** DW INVICTUS / TRANSOCEAN

Date Reached TD: 08/16/2026

06/24/2026		OH	ST01BP00	STO BLK 247 #1, LOCATION
07/08/2026	DRLG	27800	OH ST01BP00 15.2	MPD 15.4, MILLED WDW @26862-26892, STO BLK 247 #1 @26892, LWD (GR, RES, FPWD, DEN, SON)
07/15/2026	TD	30195	OH ST01BP00 14.7	MPD OFF, LWD (GR, RES, FPWD) HAVING ISSUES GETTING THROUGH WDW DURING C/O RUNS, PREP TO POLISH WDW PRIOR TO RUNNING 11 7/8LNR
07/22/2026	TD	30195	OH ST01BP00 14.7	MPD OFF, POLISHED WDW, PREP TO RUN 11 7/8LNR
07/29/2026	TD	31452	OH ST01BP00 14.7	MPD 15.35, RAN 11 7/8LNR @26621-30105, FIT 16.01, LWD (GR, RES, FPWD, SON, DEN, NEUT) WHILE @ 31150, ENCOUNTERED BITUMEN & TAR, HOLE PACKED OFF, POOH TO CHANGE TO SIMPLER SLICK BHA BEFORE DRILLING AHEAD
08/05/2026	TD	31675	OH ST01BP00 14.7	MPD 15.35, DRILLED TO 31675 W/SIMPLE LWD ARCVIS, OBSERVED STALLING, PACKED OFF, STK DP @31675, SEVERED DP, TF @31119, PREP TO BYPASS
08/12/2026	TD	31675	OH ST01BP00 14.7	MPD 15.35, PUMPED CEMENT PLUG, RIH W/10 5/8 DRILLING BHA TO BYPASS
08/19/2026	TD	31675	OH ST01BP00 14.7	MPD 15.35, TOC @29585, BYPASSED @30165
08/19/2026	TD	35454	BP1 ST01BP01 14.9	MPD 15.73, LWD (GR, RES, NBGR) POOH, WILL WL LOG

GREEN CYN

ANADARKO PETROLEUM CORPO

606

OCS: 21807

PROSPECT: K-2

WELL: 2

Status: DRLG

562 FLD

Class: DEV

SS

API: 608114080500

LOC 869' FSL & 4722' FEL **of Block** 00562 GREEN CYN

LAT = 27.38844535 (27°23'18.403") **LON** = -90.25926199 (-90°15'33.343")

X = 2,529,678 **Y** = 9,948,389 **PMD:** 28560 **PTVD:** 26448

PBHL: OH 2187' FNL & 1326' FEL **of Block** 606 GREEN CYN

ATD OH: 28025 **BP1:** **BP2:** **BP3:** **BP4:** **BP5:**

SPUD: 06/28/2026 **SUSP:**

COMP:

RR:

CSG= OH 36 @4361 302' ; 28 @5147 ; 22 @8540 FIT 13.1 ; 18LNR @8058-12865 FIT 16.6 ; 14 @22770 FIT 16.6

WD= 3979 **KB=** 80 **RIG:** DS-16 / VALARIS

Date Reached TD:

07/01/2026	TD	5290	OH ST00BP00 12.6	36 @4361 W/302'P, RAN 28 @5147, LWD (GR, RES, APWD) WOC
07/08/2026	TD	8565	OH ST00BP00 11.5	LWD (GR, RES, APWD) RAN 22 @8540, RAN RISER & BOP, REPG BOP
07/15/2026	TD	13010	OH ST00BP00 12.4	FIT 13.12 ON 22, LWD (GR, RES, APWD) PREP TO RUN 18LNR
07/22/2026	DRLG	21605	OH ST00BP00 14.3	MPD 14.9, RAN 18LNR @8058-12865, FIT 16.6, LWD (GR, RES, APWD)
07/29/2026	TD	22810	OH ST00BP00 14.3	MPD 14.8, LWD (GR, RES, APWD) RAN 14 @22770, PREP TO DRILL OUT
08/05/2026	TD	28025	OH ST00BP00 13.8	MPD 14.5, TOOK FIT 16.57 ON 14, LWD (GR, RES, SON, DEN, NEUT, GEOTAP, APWD) WHILE BACKREAMING OUT OF HOLE, DP GOT STUCK @27092, JARRING
08/12/2026	TD	28025	OH ST00BP00 13.8	MPD 14.5, JARRING UNSUCCESSFUL, SEVD DP, TF @ 26467, SET PLUGS, 26462-25462, 25124-24424, 23800-23100, 23100-22370, PREP TO BYPASS
08/19/2026	TD	28025	OH ST00BP00 13.8	MPD 14.5, BYPASSED @22903
08/19/2026	TD	26221	BP1 ST00BP01 13.8	MPD 14.47, LWD (GR, RES, FPWD, APWD) PREP TO

ACTIVE

REPAIR MPD SYSTEM

GREEN CYN	726	PROSPECT: CAESAR TONGA
ANADARKO PETROLEUM CORPO	OCS: 24179	WELL: 6 Status: DRLG

640 FLD	Class: DEV	SS	API: 608114080000
----------------	-------------------	-----------	--------------------------

LOC 6073' FSL & 4675' FWL **of Block** 00727 GREEN CYN
LAT = 27.23835119 (27°14'18.064") **LON** = -90.81889581 (-90°49'08.025")
X = 2,348,995 **Y** = 9,890,233 **PMD**: 27320 **PTVD**: 23349
PBHL: OH 13237' FSL & 5' **FEL of Block** 726 GREEN CYN
ABHL: OH **MD**: 27335 **TVD**: 23369 N 7166' @ W 4680'
ATD OH: 27335 **BP1**: **BP2**: **BP3**: **BP4**: **BP5**:

SPUD: 05/04/2026 **SUSP**: **COMP**: **RR**:
CSG= OH 36 @5127 339' ; 22 @6912 FIT 13.7 ; 18LNR @6625-13215 FIT 15.8 ;
14 @23265 FIT 15.5 ; 9 7/8LNR @27328

WD= 4707 **KB**= 81 **RIG**: OCEAN BLACKHAWK / NOBLE DRLG
Date Reached TD: 06/16/2026

04/22/2026		OH	ST00BP00	LOCATION
04/29/2026		OH	ST00BP00	BETWEEN WELL MAINTENANCE
05/06/2026	DRLG	5746	OH	ST00BP00 11.5 36 @5127 W/339'P, LWD (GR, RES, PWD)
05/13/2026	TD	6937	OH	ST00BP00 12.5 LWD (GR, RES, PWD) RAN 22 @6912, PREP TO DRILL OUT
05/20/2026	TD	13349	OH	ST00BP00 13.4 NO MPD, FIT 13.73 ON 22, LWD (GR, RES, PWD) SET 18LNR @6625-13215, WOC
05/27/2026	TD	22066	OH	ST00BP00 14.3 FIT 15.8 ON 18LNR, WHILE @19300, TOOK OPEN HOLE FIT 15.01, ROLLING OVER MUD TO 14.7, LWD (GR, RES, PWD)
06/03/2026	TD	23300	OH	ST00BP00 14.3 MPD 15.1, LWD (GR, RES, PWD) WHILE POOH, HOLE PACKED OFF, TWISTED OFF DP, TF @9068, FSG
06/10/2026	TD	23300	OH	ST00BP00 15.1 MPD OFF, RECD FSH, RNG 14
06/17/2026	TD	27335	OH	ST00BP00 14.1 MPD 14.9, RAN 14 @23265, FIT 15.49, WHILE @ 26180, TOOK DFIT 15.0, LWD (GR, RES, PWD, X-BAT, ALD, CTN, GEOTAP) C&C
06/24/2026	TD	27335	OH	ST00BP00 14.8 NO MPD, ATTEMPTED WL, NGI, DEN, NEUT, ZAIT, HIT BRDG @23315, RECONFIGURED TOOL STRING TO NGI W/A JAR TO COLLECT SAMPLES, HIT BRDG @ 23315, NO SAMP OR LOGS RECD, RAN 9 7/8LNR @ 23006-27328, WOC
06/24/2026	TD	27335	OH	ST00BP00 14.8 ANADARKO PAST THEIR PTD BY 15' WHICH PUT THE WELL IN BLK 726 INSTEAD OF 727, THIS REQUIRED ANADARKO TO CHANGE THE BLOCK, WELL & OCS # ORIG PBHL: 13248 FSL 10 FWL BLK 727, ORIG WELL #7, ORIG OCS16783
07/01/2026	TD	27335	OH	ST00BP00 14.8 NO MPD, RAN CIBP @27710, RNG 10 1/8 X 10 3/4 TB
07/08/2026	TD	27335	OH	ST00BP00 14.8 RAN 10 1/8 X 3/4 TB @23006, COMPTG
07/15/2026	TD	27335	OH	ST00BP00 14.8 COMPTG
07/22/2026	TD	27335	OH	ST00BP00 14.8 COMPTG
07/29/2026	TD	27335	OH	ST00BP00 14.8 COMPTG
08/05/2026	TD	27335	OH	ST00BP00 14.8 COMPTG
08/12/2026	TD	27335	OH	ST00BP00 14.8 COMPTG
08/19/2026	TD	27335	OH	ST00BP00 14.8 COMPTG

GREEN CYN	742	PROSPECT: ATLANTIS
BP EXPL	OCS: 15606	WELL: DC152 Status: DRLG

743 FLD	Class: DEV	API: 608114080400
----------------	-------------------	--------------------------

LOC 6582' FSL & 7050' FWL **of Block** 00743 GREEN CYN
LAT = 27.22528047 (27°13'31.010") **LON** = -90.03216544 (-90°01'55.796")
X = 2,604,810 **Y** = 9,890,742 **PMD**: 21494 **PTVD**: 17873
PBHL: OH 7636' FSL & 215' **FEL of Block** 742 GREEN CYN

ACTIVE

ATD OH: **BP1:** **BP2:** **BP3:** **BP4:** **BP5:**

SPUD: 06/24/2026 **SUSP:** **COMP:** **RR:**
CSG= OH 36 @7132 299' ; 22 @10562 ; 16 @13531 PIT 12.1 ;
 13 5/8LNR @13249-16473 PIT 12.1 ; 9 7/8LNR @16262-19955 PIT 11.7

WD= 6833 **KB=** 80 **RIG:** OCEAN BLACK HORNET / NOBLE DRLG

Date Reached TD:

06/24/2026		OH	ST00BP00	BATCH SET, 36 @7132 W/299'P, PREP TO SPUD
07/01/2026	TD	10592	OH	ST00BP00 12.0 LWD(GR, RES, PWD) RNG 22
07/08/2026	TD	10592	OH	ST00BP00 12.0 RAN 22 @10562, PREP TO DRILL OUT
07/15/2026	TD	13536	OH	ST00BP00 10.6 LWD(GR, RES, PWD, SON) RAN 16 @13531, PIT 12.1, PREP TO DRILL AHEAD
07/22/2026	TD	16641	OH	ST00BP00 11.0 MPD 11.9, LWD(GR, RES, PWD, SON) PREP TO RUN 13 5/8LNR
07/29/2026	DRLG	17047	OH	ST00BP00 10.2 MPD 10.93, RAN 13 5/8LNR @13249-16473, PIT 12.1, LWD(GR, RES, PWD, SON)
08/05/2026	DRLG	19411	OH	ST00BP00 10.2 MPD 10.5, LWD(GR, RES, PWD, SON, NEUT, GEOTAP)
08/12/2026	TD	19960	OH	ST00BP00 10.2 MPD 10.95, LWD(GR, RES, PWD, GEOTAP, SON, NEUT) PREP TO RUN 9 7/8LNR
08/19/2026	TD	19960	OH	ST00BP00 10.2 MPD 10.95, RAN 9 7/8LNR @16262-19955, PIT 11.71, PREP TO DRILL

GREEN CYN	782	PROSPECT: MAD DOG
BP EXPLORATION & PRODUCT	OCS: 15610	WELL: MD15 Status: DRLG

826 FLD **Class: DEV** **API: 608114061200**

LOC 7228' FSL & 6166' FEL **of Block** 00782 GREEN CYN
LAT = 27.18830922 (27°11'17.913") **LO**N = -90.26861424 (-90°16'07.011")
X = 2,528,234 **Y** = 9,875,548 **PMD:** 25478 **PTVD:** 22443
PBHL: OH 3471' FNL & 2401' FWL **of Block** 782 GREEN CYN
ABHL: OH **MD:** 25533 **TV**D: 22524 N 5168' @ W 7266'
ABHL: BP2 **MD:** 25781 **TV**D: 22522 N 5429' @ W 7198'
ATD OH: 25781 **BP1:** 24014 **BP2:** 25781 **BP3:** **BP4:** **BP5:**

SPUD: 11/07/2013 **SUSP:** **COMP:** **RR:**
CSG= OH 36 @4886 290' ; 22 @7094 FIT 10.8 ; 16LNR @6488-12455 FIT 15.1 ;
 14LNR @12154-19648 FIT 13.6 ; 11 7/8LNR @19443-23275 PIT 13.6 ;
 9 7/8LNR @23048-25743

WD= 4428 **KB=** 168 **RIG:** MAD DOG SPAR / VALARIS

Date Reached TD: 04/23/2026

09/11/2013		OH	ST00BP00	(APPROVED PERMIT 9-6-13) (BATCH SET)
10/09/2013		OH	ST00BP00	M/ON 10-7-13, PREP TO RUN 36"
10/16/2013		OH	ST00BP00	M/ON 10-7-13, 36 @4886W/290'P, M/OFF 10-10-13 (WILL RET)
11/13/2013	TD	7125	OH	ST00BP00 14.0 M/ON 11-6-13, LWD(GR, RES) PREP TO RUN 22"
11/20/2013	TD	7125	OH	ST00BP00 14.0 22" @7094, WOC
11/27/2013	TD	7125	OH	ST00BP00 14.0 M/OFF 11-19-13 (WILL RETURN)
12/24/2025	TD	7125	OH	ST00BP00 14.0 M/ON 12-14-25, C/O TO DRILL AHEAD
12/31/2025	DRLG	10664	OH	ST00BP00 10.1 FIT 10.79 ON 22, LWD(GR, RES, PWD)
01/07/2026	TD	12460	OH	ST00BP00 10.2 LWD(GR, RES, PWD) PREP TO RUN 16LNR
01/14/2026	TD	12460	OH	ST00BP00 10.2 16LNR @6488-12455, PREP TO DRILL OUT & TEST LNR
01/21/2026	DRLG	18287	OH	ST00BP00 13.9 FIT 15.06 ON 16LNR, LWD(GR, RES, PWD, SON, NBGR)
01/28/2026	TD	19659	OH	ST00BP00 14.1 LWD(GR, RES, PWD, SON, NBGR) RNG 14LNR
02/04/2026	TD	19659	OH	ST00BP00 14.2 14LNR @12154-19648, WOC
02/11/2026	TD	19659	OH	ST00BP00 14.2 PREP TO DRILL OUT & TEST 14LNR
02/18/2026	TD	25533	OH	ST00BP00 13.0 RTD 2-16-26, FIT 13.6 ON 14LNR, LWD(GR, RES, NBGR, PWD, DEN, NEUT, SON, FPWD) CIRC BOTTOM UP
02/25/2026	TD	25533	OH	ST00BP00 13.0 WHILE BACKREAMING OUT OF HOLE, HOLE PACKED OFF & WENT TO LOSSES, STK DP @22620, PREP TO SEVER PIPE
03/04/2026	TD	25533	OH	ST00BP00 13.0 SEVERED DP, TF @21176, PREP TO PB & BYPASS

ACTIVE

03/11/2026	TD	25533	OH	ST00BP00	13.0	REPD BOP,PREP TO BYPASS
03/18/2026	TD	25533	OH	ST00BP00	13.0	BYPASSED @19848
03/18/2026	TD	24014	BP1	ST00BP01	12.7	LWD(GR,RES,DEN,NEUT,CALP,ACOUSTIC TESTRAK) ENCOUNTERED TAR,EXPERIENCE BALLOONING & LOSSES,PULL UP TO 22810,SHUT WELL IN,C&C
03/25/2026	TD	24014	BP1	ST00BP01	12.7	PREP TO PB & BYPASS
04/01/2026	TD	24014	BP1	ST00BP01	12.7	BYPASSED @19676
04/01/2026	DRLG	23102	BP2	ST00BP02	12.7	LWD(GR,RES,PWD)ENCOUNTER TAR @23075
04/08/2026	TD	23300	BP2	ST00BP02	12.7	LWD(GR,RES,PWD)TOOLS FAILED FROM 23090-23300,PREP TO RUN 11 7/8LNR
04/15/2026	TD	23300	BP2	ST00BP02	12.7	11 7/8LNR @19443-23275,PREP TO DRILL OUT
04/22/2026	DRLG	24189	BP2	ST00BP02	12.7	PIT 13.6 ON 11 7/8LNR,LWD(GR,RES,PWD,SON)
04/29/2026	TD	25781	BP2	ST00BP02	12.7	LWD(GR,RES,PWD,SON)REAMING & HPU REPAIRS
05/06/2026	TD	25781	BP2	ST00BP02	12.7	REAMED TO 25781,RNG 9 7/8LNR
05/13/2026	TD	25781	BP2	ST00BP02	12.7	RAN 9 7/8LNR @23048-25743,PREP TO COMP
05/20/2026	TD	25781	BP2	ST00BP02	12.7	PREP TO COMP
05/27/2026	TD	25781	BP2	ST00BP02	12.7	COMPTG
06/03/2026	TD	25781	BP2	ST00BP02	12.7	COMPTG
06/10/2026	TD	25781	BP2	ST00BP02	12.7	COMPTG
06/17/2026	TD	25781	BP2	ST00BP02	12.7	COMPTG
06/24/2026	TD	25781	BP2	ST00BP02	12.7	COMPTG
07/01/2026	TD	25781	BP2	ST00BP02	12.7	COMPTG
07/08/2026	TD	25781	BP2	ST00BP02	12.7	COMPTG
07/15/2026	TD	25781	BP2	ST00BP02	12.7	COMPTG
07/22/2026	TD	25781	BP2	ST00BP02	12.7	COMPTG
07/29/2026	TD	25781	BP2	ST00BP02	12.7	COMPTG
08/05/2026	TD	25781	BP2	ST00BP02	12.7	COMPTG
08/12/2026	TD	25781	BP2	ST00BP02	12.7	COMPTG
08/19/2026	TD	25781	BP2	ST00BP02	12.7	COMPTG,WOW,LOOP CURRENT 2.5.KNOTS

GREEN CYN

807

PROSPECT: ANCHOR

CHEVRON U.S.A. INC.

OCS: 31752

WELL: AP7

Status: DRLG

807 FLD

Class: DEV

SS

API: 608114080200

LOC 4045' FSL & 4475' FWL of Block 00807 GREEN CYN

LAT = 27.15117389(27°09'04.226") LON = -91.21088317(-91°12'39.179")

X = 2,222,075 Y = 9,856,525 PMD: 33793 PTVD: 33536

PBHL: OH 4361' FSL & 6470' FWL of Block 807 GREEN CYN

ABHL: OH MD: 33710 TVD: 33482 S 211' @ E 480'

ATD OH: 33710 BP1: BP2: BP3: BP4: BP5:

SPUD: 04/28/2026 SUSP:

COMP:

RR:

CSG= OH 36 @5333 305' ; 22 @10547 FIT 11.7 ; 18LNR @10093-15575 FIT 14.0 ;
16LNR @8003-24855 FIT 16.1 ; 14LNR @24460-30040 FIT 16.2 ; 10LNR @29362-33634

WD= 4953 KB= 75 RIG: DW TITAN / TRANSOCEAN

Date Reached TD: 07/02/2026

04/29/2026		OH	ST00BP00	36 @5333 W/305'P,PREP TO SPUD
05/06/2026	TD	10577	OH	ST00BP00 11.0 LWD(NBGR)RNG 22
05/13/2026	TD	10577	OH	ST00BP00 11.0 22 @10547,RAN BOP,TSTG BOP
05/20/2026	TD	15628	OH	ST00BP00 10.7 MPD 11.26,FIT 11.7 ON 22,LWD(NBGR,ARCVIS) PREP TO RUN 18LNR
05/27/2026	DRLG	22646	OH	ST00BP00 12.3 MPD 12.77,RAN 18LNR @10093-15575,FIT 14.0, LWD(NBGR,ARCVIS)
06/03/2026	TD	24930	OH	ST00BP00 13.0 MPD 13.15,LWD(NBGR,ARCVIS)RAN 16LNR @ 8003-24855,PREP TO TEST BOP
06/10/2026	TD	30164	OH	ST00BP00 14.9 MPD 15.56,TOOK FIT 16.1 ON 16LNR,LWD(NBGR, ARCVIS)WHILE @29096 HAD LOSSES,DECREASED MPD TO 15.5,HOLE PACKED OFF,RECD DP,HAD 5 BBL GAIN,SHUT IN,PREP TO RUN 14LNR
06/17/2026	DRLG	30615	OH	ST00BP00 14.9 MPD 15.59,RAN 14LNR @24460-30040,TOOK DFIT 16.2,LWD(NBGR,ARCVIS,SONSCOPE,STETH,ADN)
06/24/2026	TD	33710	OH	ST00BP00 14.9 MPD 15.63,LWD(NBGR,ARCVIS,SONSCOPE,STETH, ADN)WHILE @33710,DP STUCK,WHILE ATTEMPTING TO POOH,DP PARTED,TF @28190,FSG

ACTIVE

UNSUCCESSFUL, SEVERED DP @32256, UNABLE TO
FREE DP, PREP TO RE-SEVER
07/01/2026 TD 33710 OH ST00BP00 14.9 MPD 15.63, SEVERED DP @32167, SET OH PLUGS,
TOC @29420, DRLG CEMENT TO BYPASS
07/08/2026 TD 33710 OH ST00BP00 14.9 MPD 15.63, BYPASSED @30160
07/08/2026 TD 33710 BP1 ST00BP01 14.9 MPD 15.63, LWD (NBGR, ARCVIS) RAN WL, HXPT, HLDS,
QCNT, PPC, MSIP @33700, LOGGING
07/15/2026 TD 33710 BP1 ST00BP01 14.9 MPD 15.63, RAN WL #2, PPC, HLDS @33600, RAN
STK & SET 10LNR @29362-33634, RNG 10 1/4 TB
07/22/2026 TD 33710 BP1 ST00BP01 14.9 MPD 15.63, RAN 10 1/4TB @29362, COMPTG
07/29/2026 TD 33710 BP1 ST00BP01 14.9 MPD 15.63, COMPTG
08/05/2026 TD 33710 BP1 ST00BP01 14.9 MPD 15.63, COMPTG
08/12/2026 TD 33710 BP1 ST00BP01 14.9 MPD 15.63, COMPTG
08/19/2026 TD 33710 BP1 ST00BP01 14.9 MPD 15.63, COMPTG

GREEN CYN
BP EXPL

825
OCS: 9981

PROSPECT: MAD DOG
WELL: 18

Status: DRLG

826 FLD

Class: INJ

API: 608114080600

LOC 1813' FSL & 3166' FWL of Block 00825 GREEN CYN
LAT = 27.13120179 (27°07'52.326") LON = -90.33869377 (-90°20'19.298")
X = 2,505,886 Y = 9,854,293 PMD: 24318 PTVD: 23342
PBHL: OH 6886' FSL & 4588' FWL of Block 825 GREEN CYN
ATD OH: BP1: BP2: BP3: BP4: BP5:

SPUD: 07/29/2026 SUSP: COMP: RR:
CSG= OH 36 @5534 271' ; 22 @7670 PIT 12.6

WD= 5182 KB= 81 RIG: OCEAN BLACKLION / NOBLE DRLG
Date Reached TD:

07/22/2026 OH ST00BP00 BATCH SET
07/29/2026 OH ST00BP00 36 @5534 W/271'P
08/05/2026 TD 7700 OH ST00BP00 10.7 LWD (GR, RES, PWD) RAN 22 @7670, REPG BOP
08/12/2026 TD 7700 OH ST00BP00 10.7 REPD BOP, RAN BOP, PREP TO DRILL OUT
08/19/2026 TD 17065 OH ST00BP00 11.1 MPD 12.5, PIT 12.57 ON 22, LWD (GR, RES, PWD)
PREP TO RUN 14

WALKER RIDGE
TALOS ENERGY OFFSHORE LL

107
OCS: 35724

PROSPECT: DAENERYS
WELL: SS2

Status: DRLG

107 WC

Class: EXP/APPR SS

API: 608124016300

LOC 5648' FSL & 5131' FEL of Block 00107 WALKER RIDGE
LAT = 26.84773226 (26°50'51.836") LON = -91.00224249 (-91°00'08.073")
X = 2,291,668 Y = 9,747,248 PMD: 30218 PTVD: 29800
PBHL: OH 7345' FNL & 5188' FEL of Block 107 WALKER RIDGE
ABHL: OH MD: 29925 TVD: 29485 N 2965' @ W 80'
ATD OH: 29925 BP1: BP2: BP3: BP4: BP5:

SPUD: 07/01/2026 SUSP: COMP: RR:
CSG= OH 36 @6316 311' ; 28 @7492 ; 22 @9808 LOT 13.8 ; 18LNR @9335-15327 FIT 15.3 ;
14 @25507 FIT 16.0 ; 11 7/8LNR @25033-27733 FIT 15.3

WD= 5923 KB= 82 RIG: WEST VELA / SEADRILL
Date Reached TD: 08/09/2026

05/13/2026 OH ST00BP00 LOCATION
07/08/2026 TD 9868 OH ST00BP00 11.5 36 @6316 W/311'P, 28 @7492, 22 @9808,
LWD (ARCVIS) RNG BOP & RISER
07/15/2026 TD 15450 OH ST00BP00 13.2 RAN BOP & RISER, TOOK LOT 13.8 ON 22,
LWD (ARCVIS) RNG 18LNR
07/22/2026 TD 25720 OH ST00BP00 14.5 MPD 14.7, RAN 18LNR @9335-15327, FIT 15.34,
LWD (ARCVIS) RNG 14
07/29/2026 TD 27930 OH ST00BP00 14.6 MPD 14.8, RAN 14 @25507, FIT 16.03,
LWD (ARCVIS, DEN, NEUT, SONSCOPE, STETH) RNG 11

ACTIVE

08/05/2026 TD 27930 OH ST00BP00 14.6 7/8LNR MPD 14.8,RAN 11 7/8LNR @25033-27733, PREP TO TAKE FIT
 08/12/2026 TD 29925 OH ST00BP00 14.5 MPD 14.8,TOOK FIT 15.31 ON 11 7/8LNR, LWD (ARCVIS, DEN, NEUT, SONSCOPE, STETH) PREP TO RUN WL LOGS
 08/19/2026 TD 29925 OH ST00BP00 14.5 MPD 14.8,RAN WL, RTSCANNER, LITHOSCANNER, GR, RES, DEN, NEUT, NGI @29925, TOOK MDTs (PRESS & SAMP) TOOK RSWC, PREP TO T/A, WELL CAN BE RE-ENTER AT A LATER DATE

WALKER RIDGE
 CHEVRON U.S.A. INC.

677
 OCS: 18753

PROSPECT: ST MALO
 WELL: PS9

Status: DRLG

678 FLD

Class: DEV

SS

API: 608124016200

LOC 4924' FNL & 261' FWL of Block 00678 WALKER RIDGE
 LAT = 26.29692250 (26°17'48.921") LON = -91.09201106 (-91°05'31.240")
 X = 2,265,381 Y = 9,546,596 PMD: 30443 PTVD: 28864
 PBHL: OH 4015' FSL & 494' FEL of Block 677 WALKER RIDGE
 ABHL: OH MD: 30400 TVD: 28835 S 6742' @ W 678'
 ATD OH: 30400 BP1: BP2: BP3: BP4: BP5:

SPUD: 04/04/2026 SUSP: COMP: RR:
 CSG= OH 36 @7452 313' ; 22 @10516 FIT 13.3 ; 14 @25658 FIT 14.6 ;
 9 7/8LNR @24454-30390 ; 9 7/8SCAB LNR @24244-24484

WD= 7038 KB= 101 RIG: DW CONQUEROR / TRANSOCEAN
 Date Reached TD: 05/06/2026

04/08/2026 TD 10556 OH ST00BP00 10.5 36 @7452 W/313'P, LWD (NBGR) RAN 22 @10516, WOC
 04/15/2026 DRLG 10585 OH ST00BP00 11.7 RAN RISER & BOP, TOOK FIT 13.3 ON 22, LWD (NBGR, ARCVIS)
 04/22/2026 DRLG 22028 OH ST00BP00 11.7 MPD 12.21, MPD FINGERPRINTING, LWD (NBGR, ARCVIS)
 04/29/2026 TD 25718 OH ST00BP00 11.7 MPD 12.3, LWD (NBGR, ARCVIS) C&C, RNG 14
 05/06/2026 DRLG 26262 OH ST00BP00 13.2 MPD 13.94, RAN 14 @25658, FIT 14.6, LWD (ARCVIS, SADN, STETH, SONSCOPE)
 05/13/2026 TD 30400 OH ST00BP00 13.2 MPD 13.9, LWD (ARCVIS, SADN, STETH, SONSCOPE) RAN 9 7/8LNR @24454-30390, WOC
 05/20/2026 TD 30400 OH ST00BP00 13.2 MPD 13.9, MADE UNSUCCESSFUL ATTEMPTS TO SET LNR-TOP PLUG & TA PKR, PREP TO SET TA CEMENT PLUG, WILL RELEASE RIG & RETURN TO COMP AT A LATER DATE
 05/27/2026 TD 30400 OH ST00BP00 13.2 MPD 13.9, SET CEMENT PLUG, TOC @23887, R.R.5-24-26
 07/29/2026 TD 30400 OH ST00BP00 13.2 MPD 13.9, M/ON 7-24-26, PREP TO DRILL OUT PLUGS, RUN SCAB LNR & COMP
 08/05/2026 TD 30400 OH ST00BP00 13.2 MPD 13.9, RAN 9 7/8SCAB LNR @24244-24484, PREP TO COMP
 08/12/2026 TD 30400 OH ST00BP00 13.2 MPD 13.9, PREP TO COMP
 08/19/2026 TD 30400 OH ST00BP00 13.2 MPD 13.9, COMPTG

MISSISSIPPI CYN
 SHELL

477
 OCS: 36962

PROSPECT: SISCO
 WELL: 1

Status: DRLG

477 WC

Class: EXP

API: 608174152600

LOC 6170' FSL & 5791' FWL of Block 00477 MISSISSIPPI CYN
 LAT = 28.51480163 (28°30'53.286") LON = -88.14444392 (-88°08'39.998")
 X = 1,272,991 Y = 10,349,690 PMD: 30605 PTVD: 30522
 PBHL: OH 5332' FSL & 5306' FWL of Block 477 MISSISSIPPI CYN
 ATD OH: BP1: BP2: BP3: BP4: BP5:

SPUD: 06/22/2026 SUSP: COMP: RR:
 CSG= OH 38 @7132 197' ; 28 @8586 ; 22 @12775 FIT 12.1 ; 18LNR @12600-19039 FIT 14.1

ACTIVE

WD= 6833 KB= 102 RIG: DW PONTUS / TRANSOCEAN

Date Reached TD:

06/10/2026		OH	ST00BP00	LOCATION
06/24/2026 TD	8640	OH	ST00BP00 8.6	MPD OFF,RAN 38 @7132 W/197'P,LWD(EWR-M5) PREP TO RUN 28
07/01/2026 TD	12839	OH	ST00BP00 13.6	MPD OFF,LWD(EWR-M5)RAN 28 @8586,RAN 22 @ 12775,RNG RISER & BOP
07/08/2026 DRLG	15780	OH	ST00BP00 12.1	CML 11.8,TOOK FIT 12.1 ON 22,LWD(BASESTAR, RESISTAR,XBAT)
07/15/2026 TD	19200	OH	ST00BP00 12.1	CML 11.9,LWD(BASESTAR,RESISTAR,XBAT)RAN 18LNR @12600-19039,WOC
07/22/2026 TD	21875	OH	ST00BP00 13.4	CML 13.48,TOOK FIT 14.1 ON 18LNR,LWD(GR, RESISTAR,PWD,DEN,NEUT,X-BAT,GEOTAP)WOW
07/29/2026 TD	22795	OH	ST00BP00 13.4	CML 13.4,LWD(GR,RESISTAR,PWD,DEN,NEUT, X-BAT,GEOTAP)PERFORMED OPEN HOLE FIT 14.1 @ 22749,POOH TO TEST BOP
08/05/2026 DRLG	24025	OH	ST00BP00 14.1	CML 13.95,LWD(GR,RESISTAR,PWD,DEN,NEUT, X-BAT,GEOTAP)
08/12/2026 TD	26318	OH	ST00BP00 14.0	CML 13.95,LWD(GR,RESISTAR,PWD,DEN,NEUT, X-BAT,GEOTAP)PULLED BHA DUE TO SLOW DRILLING,ON TRIP FOR NEW BHA
08/19/2026 DRLG	26995	OH	ST00BP00 14.9	WHILE @26995,MUD 14.9,CML 15.2,LWD(GR,PWD, DEN,NEUT,RESISTAR,XBAT,GEOTAP)RAN 12.25 X 11.97 @26909,FIT 15.42,DRILING W/LWD(ABGR, GR,PWD,SON,LITHOSTAR,RESISTAR,GEOTAP)

MISSISSIPPI CYN

807

PROSPECT: MARS

SHELL

OCS: 7963

WELL: A23ST3

Status: DRLG

807 FLD

Class: INJ

API: 608174049403

LOC 3657' FNL & 5612' FWL of Block 00807 MISSISSIPPI CYN
 LAT = 28.16944737(28°10'10.011") LON = -89.22300178(-89°13'22.806")

X = 924,332 Y = 10,228,983 PMD: 18621 PTV: 15777

PBHL: OH 3657' FNL & 5612' FWL of Block 807 MISSISSIPPI CYN

ATD OH: BP1: BP2: BP3: BP4: BP5:

SPUD: 08/05/2026 SUSP:

COMP:

RR:

CSG= OH OLD(36 @3224 ; 26 @4311 ; 20 @5377 ; 16 @7105 ; 14LNR @6491-9120 ; 13 3/8LNR
 @6191-13115 ; 11 7/8LNR @9092-13572)
 7 5/8LNR @12339-17830

WD= 2945 KB= 191 RIG: H&P 201 / H&P DRLG

Date Reached TD:

08/12/2026 TD	17835	OH	ST03BP00 12.1	MPD 12.9,STO #A-23ST2 @14798,LWD(ONTRAK) PREP TO RUN 7 5/8LNR
08/19/2026 TD	17835	OH	ST03BP00 12.1	MPD 12.9,RAN 7 5/8LNR @12339-17830,PREP TO RUN TB

MISSISSIPPI CYN

816

PROSPECT: TAGGART

LLOG EXPL

OCS: 33178

WELL: 4

Status: DRLG

816 FLD

Class: DEV

API: 608174152700

LOC 4336' FNL & 2732' FEL of Block 00816 MISSISSIPPI CYN
 LAT = 28.17434987(28°10'27.660") LON = -88.75734280(-88°45'26.434")

X = 1,074,388 Y = 10,228,304 PMD: 13568 PTV: 11112

PBHL: OH 6768' FNL & 5931' FEL of Block 816 MISSISSIPPI CYN

ATD OH: 13400 BP1: BP2: BP3: BP4: BP5:

SPUD: 07/13/2026 SUSP:

COMP:

RR:

CSG= OH 36 @6023 304' ; 28 @7274 ; 22 @8498 FIT 11.0 ; 13 5/8 @10579 FIT 12.1 ;
 9 7/8LNR @10329-13398

ACTIVE

WD= 5637 **KB=** 82 **RIG:** WEST NEPTUNE / SEADRILL**Date Reached TD:** 08/13/2026

07/01/2026		OH	ST00BP00		LOCATION
07/15/2026		OH	ST00BP00		RIGGING UP
07/22/2026	TD	8540	OH	ST00BP00	10.7 36 @6023 W/304'P, 28 @7274, LWD (ONTRAK) 22 @ 8498, WOW
07/29/2026	TD	8550	OH	ST00BP00	9.5 ATTEMPTED LOT ON 22, TEST FAILED, SQUEEZING 22
08/05/2026	TD	9456	OH	ST00BP00	10.1 TOOK FIT 10.98 ON 22, LWD (ONTRAK) WOW, LOOP CURRENT 3.5-4.0 KNOTS
08/12/2026	DRLG	11317	OH	ST00BP00	11.0 WHILE @10625, MW 10.3, LWD (ONTRAK) RAN 13 5/8 @10579, FIT 12.12, LWD (ONTRAK, CCN, ORD, TESTRAK, SOUNDTRAK)
08/19/2026	TD	13400	OH	ST00BP00	11.2 LWD (ONTRAK, CCN, ORD, TESTRAK, SOUNDTRAK) RAN 9 7/8 LNR @10329-13398, PREP TO R.R. WOW, LOOP CURRENT 3.5 KNOTS



WELLS REACHING TD

KEATHLEY CYN	291	PROSPECT: WEST BUMP
BP EXPL	OCS: 19545	WELL: 2ST
		Status: DRLG

291 WC	Class: EXP	SS	API: 608084008001
---------------	-------------------	-----------	--------------------------

LOC 4687' FNL & 363' FWL **of Block** 00291 KEATHLEY CYN
LAT = 26.70216182 (26°42'07.783") **LON** = -92.63787509 (-92°38'16.350")
X = 1,758,603 **Y** = 9,689,393 **PMD**: 36146 **PTVD**: 33517
PBHL: OH 3808' FNL & 5334' FWL **of Block** 291 KEATHLEY CYN
ATD OH: 31675 **BP1**: 35454 **BP2**: **BP3**: **BP4**: **BP5**:

SPUD: 07/01/2026 **SUSP**: **COMP**: **RR**:
CSG= OH OLD(36 @6100 ; 28 @8160 ; 22 @9979 ; 18LNR @9753-14850 ; 16LNR @5847-20978 ; 14 @27696 ; 11 7/8LNR @21122-29801)
 11 7/8LNR @26621-30105 FIT 16.0

WD= 5722 **KB**= 104 **RIG**: DW INVICTUS / TRANSOCEAN
Date Reached TD: 08/16/2026

06/24/2026		OH	ST01BP00	STO BLK 247 #1, LOCATION
07/08/2026 DRLG	27800	OH	ST01BP00 15.2	MPD 15.4, MILLED WDW @26862-26892, STO BLK 247 #1 @26892, LWD (GR, RES, FPWD, DEN, SON)
07/15/2026 TD	30195	OH	ST01BP00 14.7	MPD OFF, LWD (GR, RES, FPWD) HAVING ISSUES GETTING THROUGH WDW DURING C/O RUNS, PREP TO POLISH WDW PRIOR TO RUNNING 11 7/8LNR
07/22/2026 TD	30195	OH	ST01BP00 14.7	MPD OFF, POLISHED WDW, PREP TO RUN 11 7/8LNR
07/29/2026 TD	31452	OH	ST01BP00 14.7	MPD 15.35, RAN 11 7/8LNR @26621-30105, FIT 16.01, LWD (GR, RES, FPWD, SON, DEN, NEUT) WHILE @ 31150, ENCOUNTERED BITUMEN & TAR, HOLE PACKED OFF, POOH TO CHANGE TO SIMPLER SLICK BHA BEFORE DRILLING AHEAD
08/05/2026 TD	31675	OH	ST01BP00 14.7	MPD 15.35, DRILLED TO 31675 W/SIMPLE LWD ARCVIS, OBSERVED STALLING, PACKED OFF, STK DP @31675, SEVERED DP, TF @31119, PREP TO BYPASS
08/12/2026 TD	31675	OH	ST01BP00 14.7	MPD 15.35, PUMPED CEMENT PLUG, RIH W/10 5/8 DRILLING BHA TO BYPASS
08/19/2026 TD	31675	OH	ST01BP00 14.7	MPD 15.35, TOC @29585, BYPASSED @30165
08/19/2026 TD	35454	BP1	ST01BP01 14.9	MPD 15.73, LWD (GR, RES, NBGR) POOH, WILL WL LOG

MISSISSIPPI CYN	816	PROSPECT: TAGGART
LLOG EXPL	OCS: 33178	WELL: 4
		Status: DRLG

816 FLD	Class: DEV	API: 608174152700
----------------	-------------------	--------------------------

LOC 4336' FNL & 2732' FEL **of Block** 00816 MISSISSIPPI CYN
LAT = 28.17434987 (28°10'27.660") **LON** = -88.75734280 (-88°45'26.434")
X = 1,074,388 **Y** = 10,228,304 **PMD**: 13568 **PTVD**: 11112
PBHL: OH 6768' FNL & 5931' FEL **of Block** 816 MISSISSIPPI CYN
ATD OH: 13400 **BP1**: **BP2**: **BP3**: **BP4**: **BP5**:

SPUD: 07/13/2026 **SUSP**: **COMP**: **RR**:
CSG= OH 36 @6023 304' ; 28 @7274 ; 22 @8498 FIT 11.0 ; 13 5/8 @10579 FIT 12.1 ;
 9 7/8LNR @10329-13398

WD= 5637 **KB**= 82 **RIG**: WEST NEPTUNE / SEADRILL
Date Reached TD: 08/13/2026

07/01/2026		OH	ST00BP00	LOCATION
07/15/2026		OH	ST00BP00	RIGGING UP
07/22/2026 TD	8540	OH	ST00BP00 10.7	36 @6023 W/304' P, 28 @7274, LWD (ONTRAK) 22 @ 8498, WOW
07/29/2026 TD	8550	OH	ST00BP00 9.5	ATTEMPTED LOT ON 22, TEST FAILED, SQUEEZING 22
08/05/2026 TD	9456	OH	ST00BP00 10.1	TOOK FIT 10.98 ON 22, LWD (ONTRAK) WOW,

WELLS REACHING TD

08/12/2026	DRLG	11317	OH	ST00BP00	11.0	LOOP CURRENT 3.5-4.0 KNOTS WHILE @10625,MW 10.3,LWD(ONTRAK)RAN 13 5/8 @10579,FIT 12.12,LWD(ONTRAK,CCN,ORD, TESTRAK,SOUNDTRAK)
08/19/2026	TD	13400	OH	ST00BP00	11.2	LWD(ONTRAK,CCN,ORD,TESTRAK,SOUNDTRAK)RAN 9 7/8LNR @10329-13398,PREP TO R.R.WOW,LOOP CURRENT 3.5 KNOTS



SUSPENDEDALAMINOS CYN
SHELL728
OCS: 31195PROSPECT: WHALE
WELL: WN103

Status: SUSP

728 WC

Class: DEV

API: 608054011900

LOC 1627' FSL & 3169' FEL of Block 00728 ALAMINOS CYN
 LAT = 26.23005494 (26°13'48.198") LON = -94.72843942 (-94°43'42.382")
 X = 1,073,951 Y = 9,521,467 PMD: 23560 PTVD: 21452
 PBHL: OH 7352' FSL & 4941' FEL of Block 728 ALAMINOS CYN
 PBHL: BP17366' FSL & 4955' FEL of Block 728 ALAMINOS CYN
 ABHL: BP1 MD: 23590 TVD: 21460 N 5783' @ W 1792'
 ATD OH: 19877 BP1: 23590 BP2: BP3: BP4: BP5:

SPUD: 11/03/2025 SUSP: 08/16/2026 COMP: RR: 08/16/2026
 CSG= OH 38 @8931 198' ; 28 @9843 ; 22 @14790 FIT 12.0 ;
 16.08LNR @14387-16395 FIT 12.1 ; 14LNR @16060-19547 FIT 12.6 ;
 9 5/8LNR @19245-23585

WD= 8631 KB= 102 RIG: DW POSEIDON / TRANSOCEAN
 Date Reached TD: 07/06/2026

10/15/2025		OH	ST00BP00	BATCH SET
11/12/2025	DRLG	14828	OH	ST00BP00 10.0 MPD 10.62, RAN 38 @8931 W/198'P, 28 @9843, LWD (GR, RES, PWD)
11/19/2025	TD	14840	OH	ST00BP00 10.5 MPD 10.73, LWD (GR, RES, PWD) 22 @14790, M/OFF 11-13-25, WILL RETURN
05/20/2026	TD	14840	OH	ST00BP00 10.5 M/ON 5-14-26, RNG BOP & RISER TO RESUME DRILLING OPERATIONS
05/27/2026	TD	19877	OH	ST00BP00 10.4 MPD 10.94, TOOK FIT 12.06 ON 22, LWD (ARCVIS, SONSCOPE) PREP TO RUN 13 5/8
06/03/2026	TD	19877	OH	ST00BP00 10.4 MPD 10.94, ATTEMPTED TO RUN 13 5/8, COULD NOT GET DOWN, PREP TO C/O & RE-RUN 13 5/8
06/10/2026	TD	19877	OH	ST00BP00 10.8 MPD 10.9, C/O, ATTEMPTED TO RE-RUN 13 5/8, COULD NOT GET DOWN, POOH W/CSG STRING
06/17/2026	TD	19877	OH	ST00BP00 10.8 MPD 10.9, POOH W/13 5/8LNR, PUMPED CEMENT PLUGS @14684, PREP TO BYPASS
06/24/2026	TD	19877	OH	ST00BP00 10.8 MPD 10.9, BYPASSED @14850
06/24/2026	TD	16450	BP1	ST00BP01 10.5 MPD 10.7, TOOK FIT 12.04 ON 22, LWD (ARCVIS) RAN 16.08LNR @14387-16395, PREP TO DRILL OUT, ORIG HOLE PTD: 23534 MD, 21448 TVD
07/01/2026	TD	19665	BP1	ST00BP01 11.2 MPD 11.4, TOOK FIT 12.07 ON 16.08LNR, LWD (ARCVIS) RAN 14LNR @16060-19547, PREP TO DRILL OUT
07/08/2026	TD	23590	BP1	ST00BP01 9.5 MPD 10.3, TOOK FIT 12.61 ON 14, LWD (ARCVIS, SONSCOPE, STETH, SADN) C&C, TAKING FPWD PRESSURES
07/15/2026	TD	23590	BP1	ST00BP01 9.5 MPD 10.3, TOOK FPWD PRESSURES, PERFORMED OPEN HOLE LOT TO 12.12, RAN WL, HDRS, HNGS, PPC, MAST, NGI @23590, RAN 9 5/8LNR @ 19245-23585, PREP TO RUN 9 5/8 X 10 3/4TB
07/22/2026	TD	23590	BP1	ST00BP01 9.5 MPD 10.3, RAN 9 5/8 X 10 3/4TB @19255, C/O, PREP TO COMP
07/29/2026	TD	23590	BP1	ST00BP01 9.5 MPD 10.3, COMPTG
08/05/2026	TD	23590	BP1	ST00BP01 9.5 MPD 10.3, COMPTG
08/12/2026	TD	23590	BP1	ST00BP01 9.5 MPD 10.3, COMPTG
08/19/2026	TD	23590	BP1	ST00BP01 9.5 MPD 10.3, R.R. PERFORMING END OF WELL MAINTENANCE

SUSPENDED
